

Project and Program Management Department



Project Status Report

March 31, 2017

The following is a status update of the project, reporting on key elements of progress and scheduling. This report has been prepared by the Georgia World Congress Center Authority.

1) Status of Contract Deliverables.

- Formal submission of the 100% CDs from StadCo have now been turned over.
- GWCCA has received final design peer reviews for exterior skin and mechanized roof.

2) Design/Procurement/Permitting.

- Complete

3) Budget/Cost Status.

- StadCo has issued change orders to HHRM for various scope changes. Changes are funded by project contingency. Total project cost is projected to be \$1.5B.

Project and Program Management Department



4) MBS Schedule Status and Progression.

- Subsequent work, such as ground assembly of petal pieces, and field modifications for all roof structural pieces continue.
- The catwalk and decking portion of the roof are still in installation.
- Metal panel work continues around the building at hoods and shoulders of the building.
- There is an on-going execution of field work modifications to roof steel.
- The mid-section of the petals on the operable roof are currently being erected and installed.
- Concourse 1 aisle installation is ongoing while the wall coverings go up in the corridors
- Permanent wood doors are being installed along with glass rail posts in the tub of the lower suites. Carpet and mill work also continue to progress.
- Stadium seating installation on concourse 2 is in progress.
- "Mercedes-Benz Stadium" signage is being installed on facet 4.
- Work is commencing on installation of conduit and sports lighting on roof trusses and catwalk.
- Work has commenced on the curved wall video board at the "Falcons Feather" on concourse 1.
- Ceiling grid and floor/wall tile continue to make progress on Concourse 2.
- Operable suite front installation and glazing at national/press area has begun.
- Work is being done for the installation of the bowl duct and the overhead fire protection.

Project and Program Management Department



5) Phase One Parking Deck Schedule Status.

- All first phase of punch list items have been completed.
- Construction of the pedestrian bridge has been completed.

6) Quality Assurance.

- All MBS work is being carefully inspected and documented for "Non-Conforming Work". Non-conforming MBS work is being addressed in a reasonable timeframe by contractors and remedial work reviewed by appropriate inspector (Langan/AMEC) and then approved by Architect and Engineer.

7) 30 Day Look Ahead of Scheduled Activities

- Operable roof petals to continue erection and installation.
- Surveying and analysis of steel and associated work to continue.
- Structural steel installation for the "Halo" board to continue.
- ETFE installation to continue on the exterior of the facility.
- Exterior metal panel installation to continue on roof and all sides of the facility.
- Continue painting and associated finished to concourse levels.
- Continue hardscape installation of exterior grounds. Overhead utilities to be installed under the extended plaza.
- Vertical transportation elements to continue to be commissioned and placed into service.
- Continue installation of Audio/Video components throughout the facility.

Project and Program Management Department



Project and Program Management Department




MERCEDES-BENZ STADIUM PROJECT
Atlanta, Georgia

MAR 23 2017

Project and Program Management Department



Project and Program Management Department



MERCEDES-BENZ STADIUM PROJECT
Atlanta, Georgia

MAR 23 2017


Project and Program Management Department



MERCEDES-BENZ STADIUM PROJECT
Atlanta, Georgia

MAR 23 2017

Project and Program Management Department

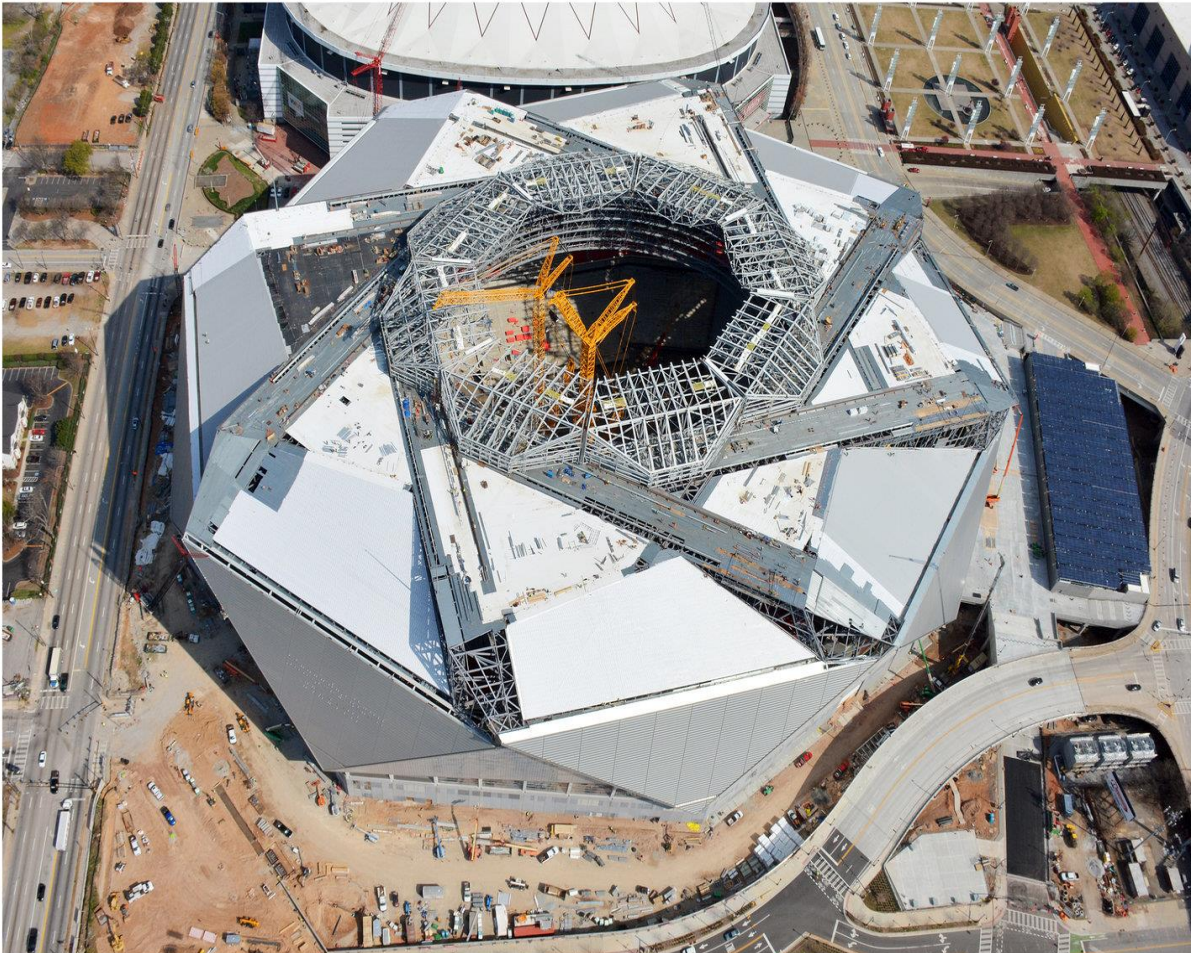

MERCEDES-BENZ STADIUM PROJECT
Atlanta, Georgia

MAR 23 2017

Project and Program Management Department



MERCEDES-BENZ STADIUM PROJECT
Atlanta, Georgia

MAR 23 2017

Project and Program Management Department



MERCEDES-BENZ STADIUM PROJECT
Atlanta, Georgia

MAR 23 2017

Project and Program Management Department



MERCEDES-BENZ STADIUM PROJECT
Atlanta, Georgia

MAR 23 2017

Project and Program Management Department



Completion of Report
