

Project and Program Management Department



Project Status Report

May 31, 2017

The following is a status update of the project, reporting on key elements of progress and scheduling. This report has been prepared by the Georgia World Congress Center Authority.

1) Status of Contract Deliverables.

- Formal submission of the 100% CDs from StadCo have now been turned over.
- GWCCA has received final design peer reviews for exterior skin and mechanized roof.

2) Design/Procurement/Permitting.

- Complete

3) Budget/Cost Status.

- StadCo has issued change orders to HHRM for various scope changes. Changes are funded by project contingency. Total project cost is projected to be at least \$1.5B.

Project and Program Management Department



4) MBS Schedule Status and Progression.

- Metal panel work continues at the hoods and shoulders of the building.
- Final detailing for skin of the operable roof is ongoing along with load verifications to support Construction move #2.
- ETFE pillows on the operable roof petals have begun on petals 2A/2B.
- On the skin of the stadium, ETFE completion list work and cable pocket cleaning is being done.
- CMU walls are still progressing in the inner bowl at the same time as the floor/wall tile for the locker rooms.
- Retractable seating installation is ongoing on the field level.
- Marble installation has started in the suites on concourse 1.
- Finishes are beginning in the Team Store on concourse 1.
- Carpet and mill work also continue to progress throughout the facility.
- Interior Sponsorship finishes are ongoing on the Lower Suite Level.
- Stadium seating installation on concourse 2 continues.
- Halo board installation has begun and testing of the video board on the mega column has commenced.

5) Phase One Parking Deck Schedule Status.

- All first phase of punch list items have been completed.
- Construction of the pedestrian bridge has been completed.

Project and Program Management Department



6) Quality Assurance.

- All MBS work is being carefully inspected and documented for “Non-Conforming Work” . Non-conforming MBS work is being addressed in a reasonable timeframe by contractors and remedial work reviewed by appropriate inspector (Langan/AMEC) and then approved by Architect and Engineer.

7) 30 Day Look Ahead of Scheduled Activities

- ETFE pillows on the operable roof petals to continue erection and installation.
- Surveying and analysis of steel and associated work to continue.
- Video panel installation for the “Halo” board to continue.
- Exterior metal panel installation to continue on roof and all sides of the facility.
- Continue painting and associated finishes to concourse levels.
- Continue hardscape installation of exterior grounds. Overhead utilities to continue being installed under the extended plaza.
- Continue installation of Audio/Video components and their associated testing throughout the facility.

Project and Program Management Department



Project and Program Management Department



MERCEDES-BENZ STADIUM PROJECT
Atlanta, Georgia

MAY 25 2017

Project and Program Management Department



MERCEDES-BENZ STADIUM PROJECT
Atlanta, Georgia

MAY 25 2017

Project and Program Management Department



MERCEDES-BENZ STADIUM PROJECT
Atlanta, Georgia

MAY 25 2017

Project and Program Management Department



MERCEDES-BENZ STADIUM PROJECT
Atlanta, Georgia

MAY 25 2017

Project and Program Management Department



MERCEDES-BENZ STADIUM PROJECT
Atlanta, Georgia

MAY 25 2017

Project and Program Management Department



MERCEDES-BENZ STADIUM PROJECT
Atlanta, Georgia

MAY 25 2017


Project and Program Management Department



MERCEDES-BENZ STADIUM PROJECT
Atlanta, Georgia

MAY 25 2017

Project and Program Management Department

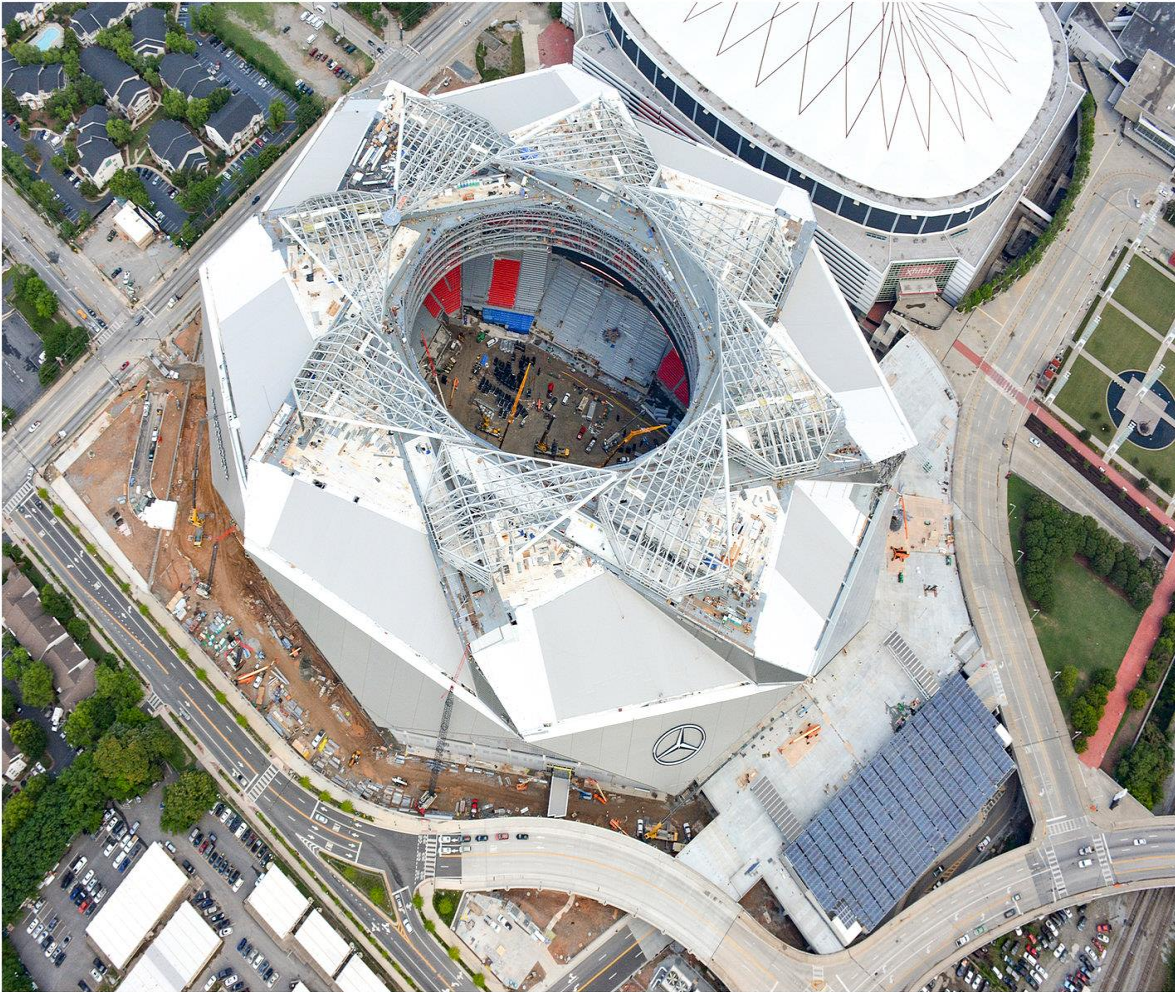

MERCEDES-BENZ STADIUM PROJECT
Atlanta, Georgia

MAY 25 2017

Project and Program Management Department



Completion of Report
