

GWCCA Campus Development Project Updates

July 8, 2021

Department of Project & Program Management

Today's Agenda

AYIB Pedestrian Mall
AYIB Transportation Depot
FY21 Roofing Replacements
Signia by Hilton
GWCCA & Hilton Sales Offices
Bldg. C Construction Graphics

Andrew Young International Blvd.

Pedestrian Mall

• Project Information

- Project Manager: Ken Stockdell
- Project Scope: Extend COP pedestrian experience to GWCC building entrances and eventually leading to GWCCA Hotel. Create a safer pedestrian experience through the GWCCA Campus.
- Project Location: Current sidewalks & traffic lanes along Andrew Young International Blvd from Marietta St. to Centennial Olympic Park Drive.

• Project Status

- Current Phase: Construction
- Construction Schedule: Mid-March December 2021


Transportation Depot

• **Project Information**


- Project Manger: Ken Stockdell
- Project Scope: Create a designated pick-up and drop-off area for all buses and taxi/rideshare vehicles. To improve traffic conditions by minimizing congestion and improving trip times.
- Project location: Current green space between International Plaza and State Farm Drive and current Red Deck Entry & COP Drive.

• Project Status

- Current Phase: Construction
- Construction Schedule: April 2021 April 2022

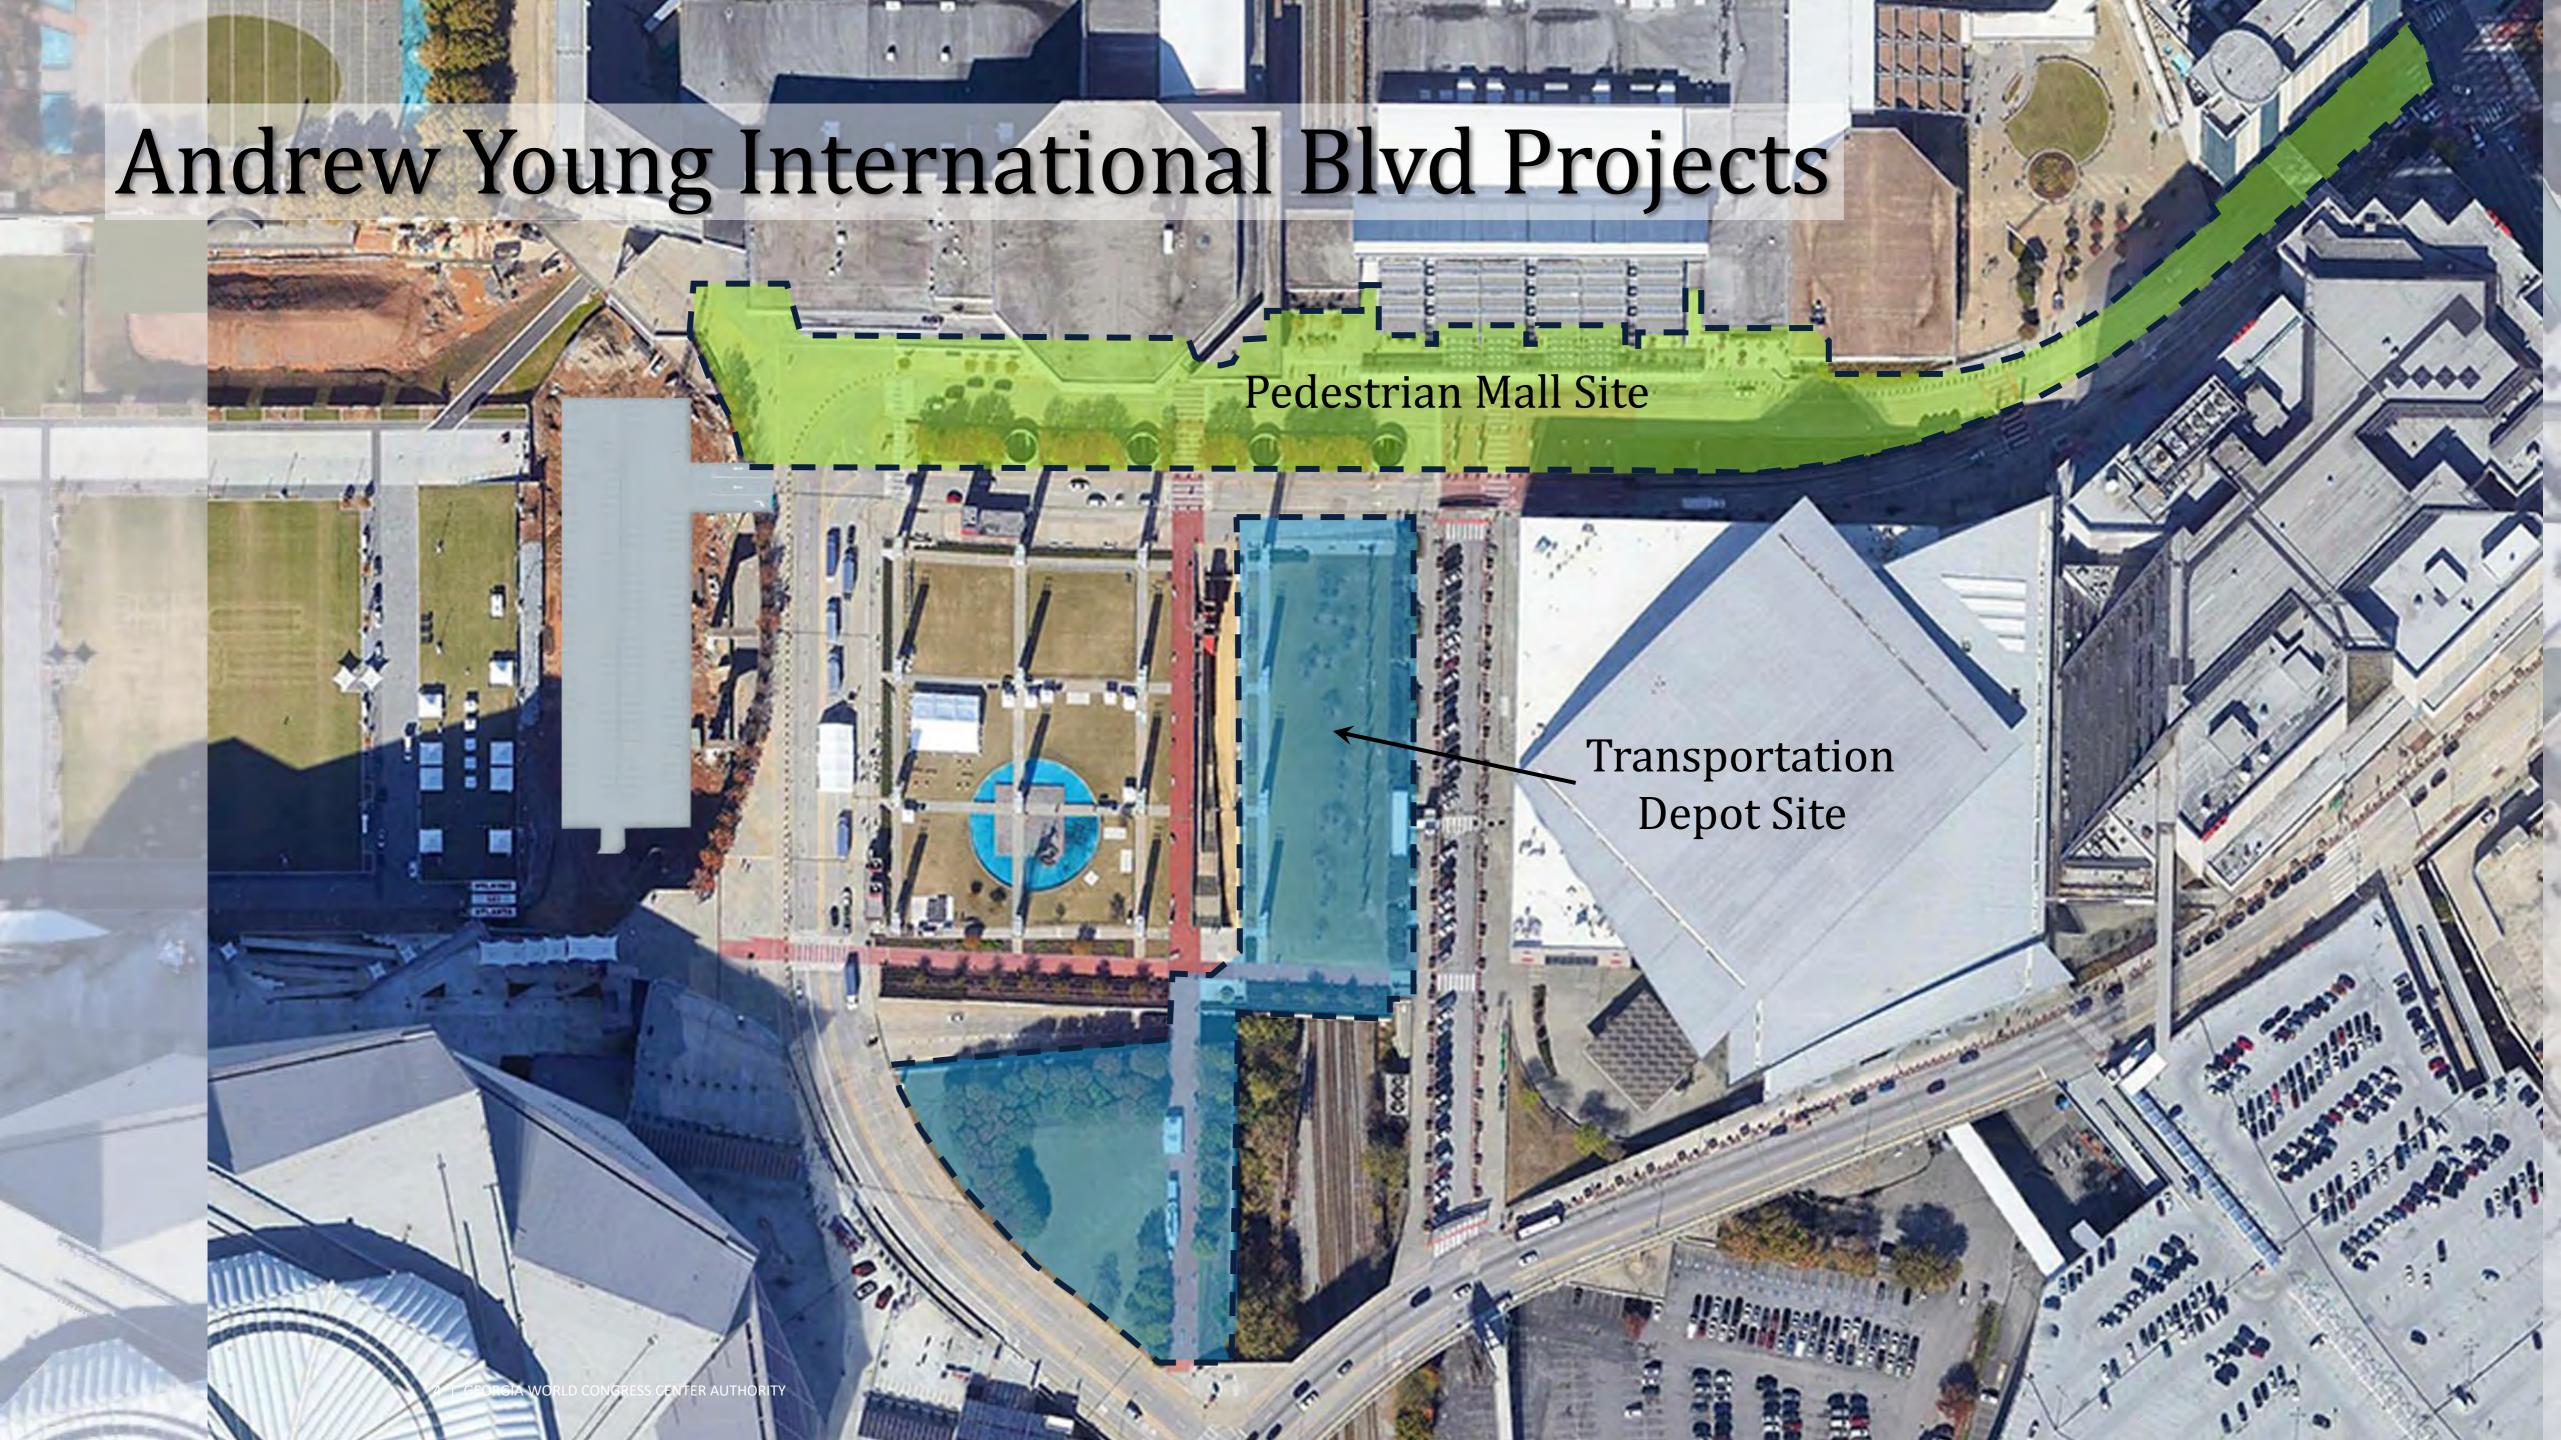




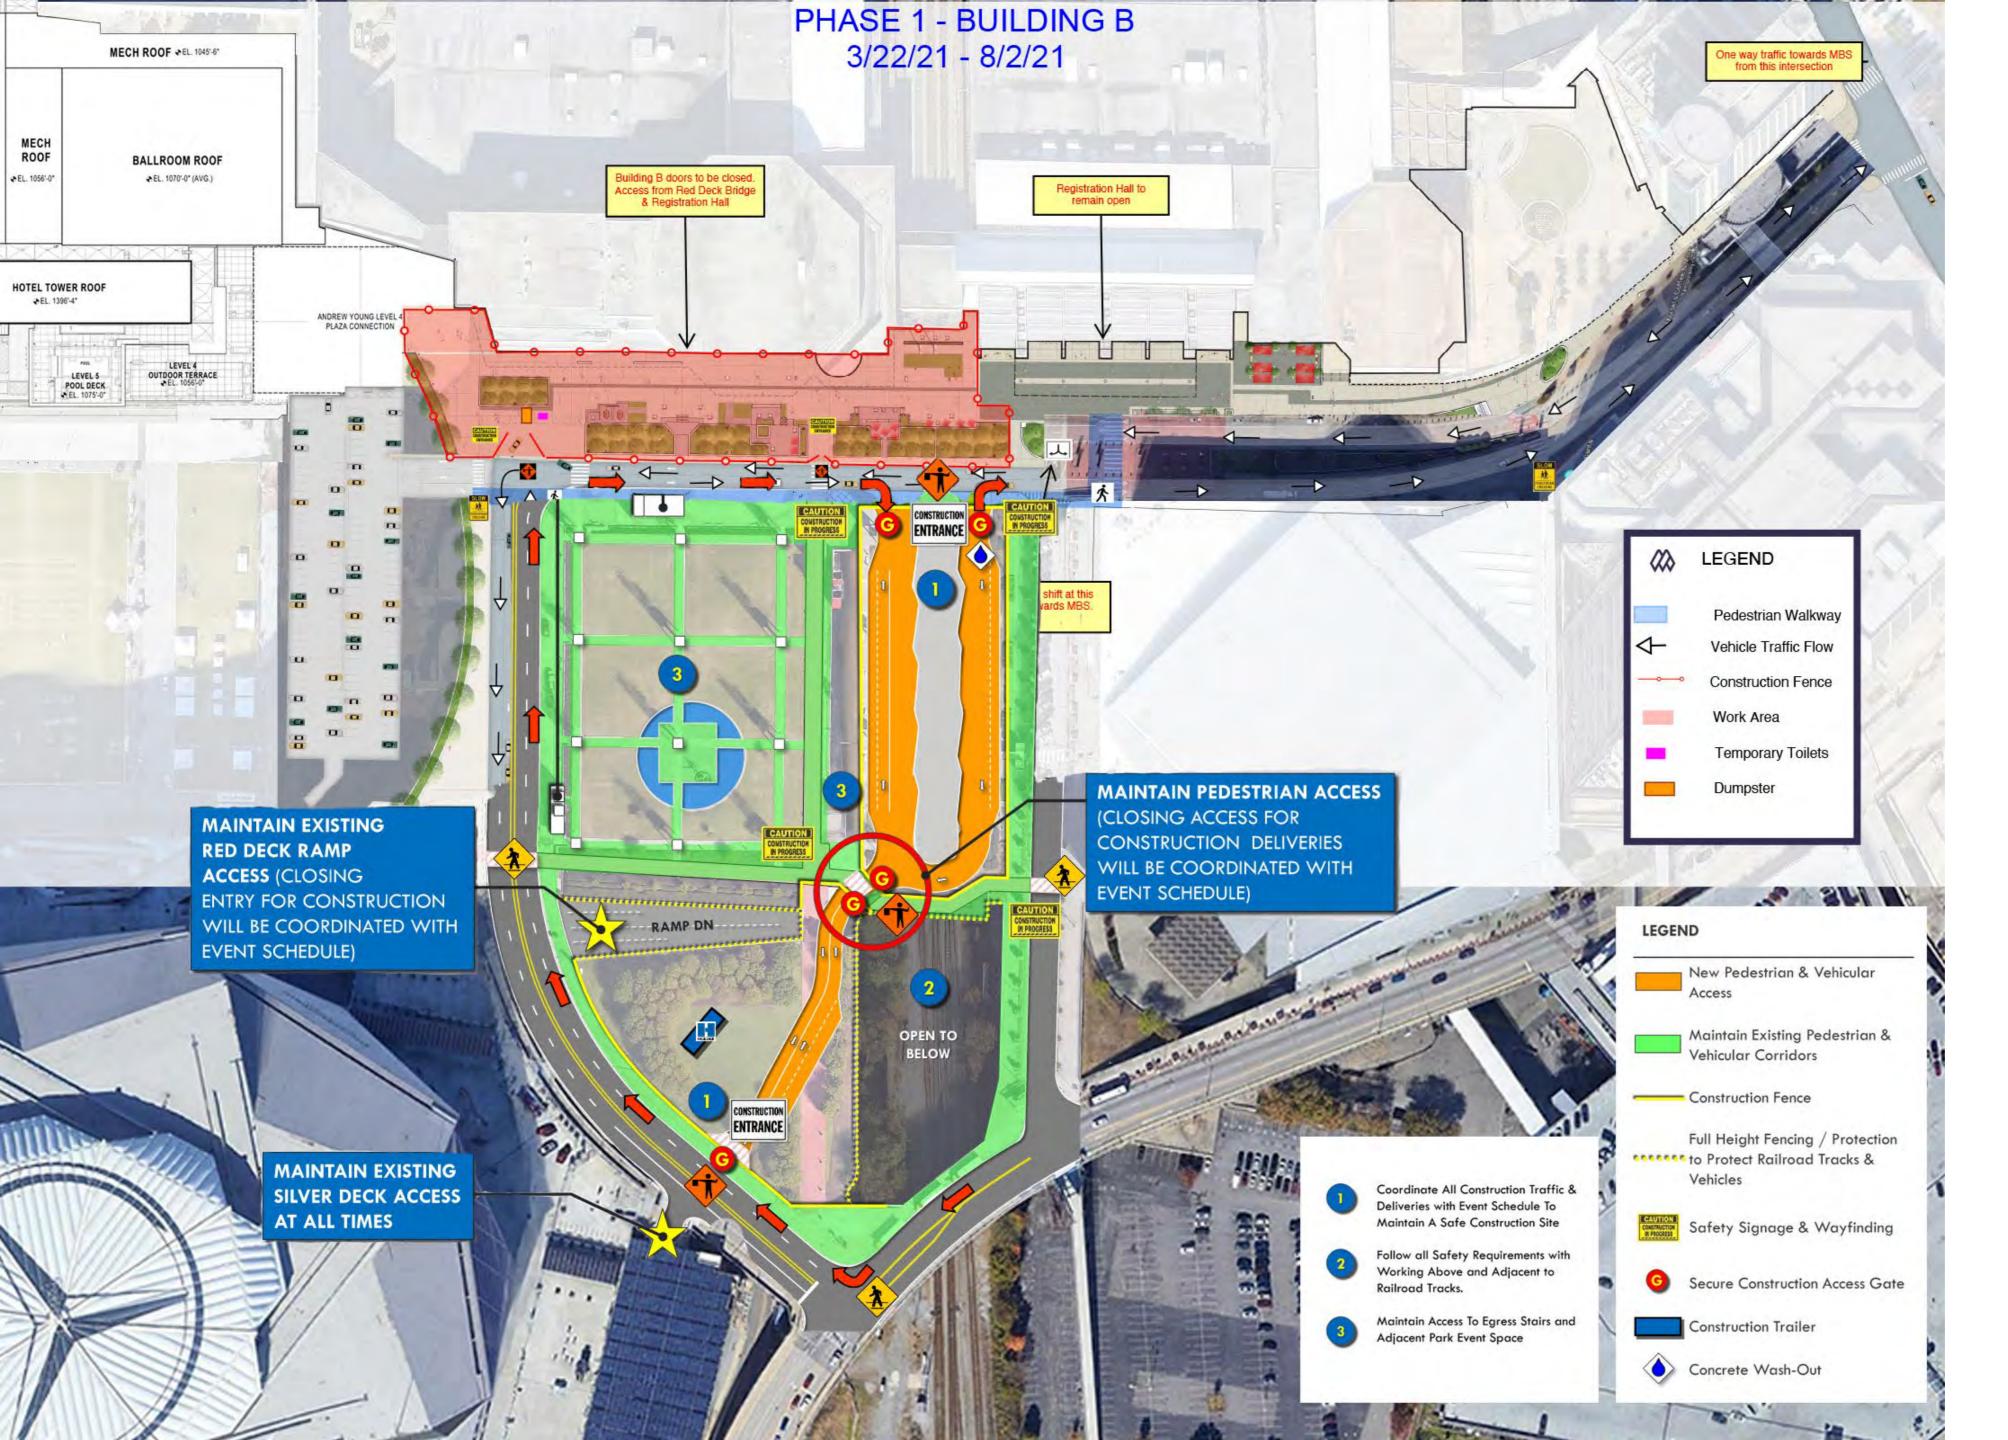

Pedestrian Mall
Phase 1
3/22/21 - 8/2/21

Transportation Depot 4/6/21 - 4/5/22

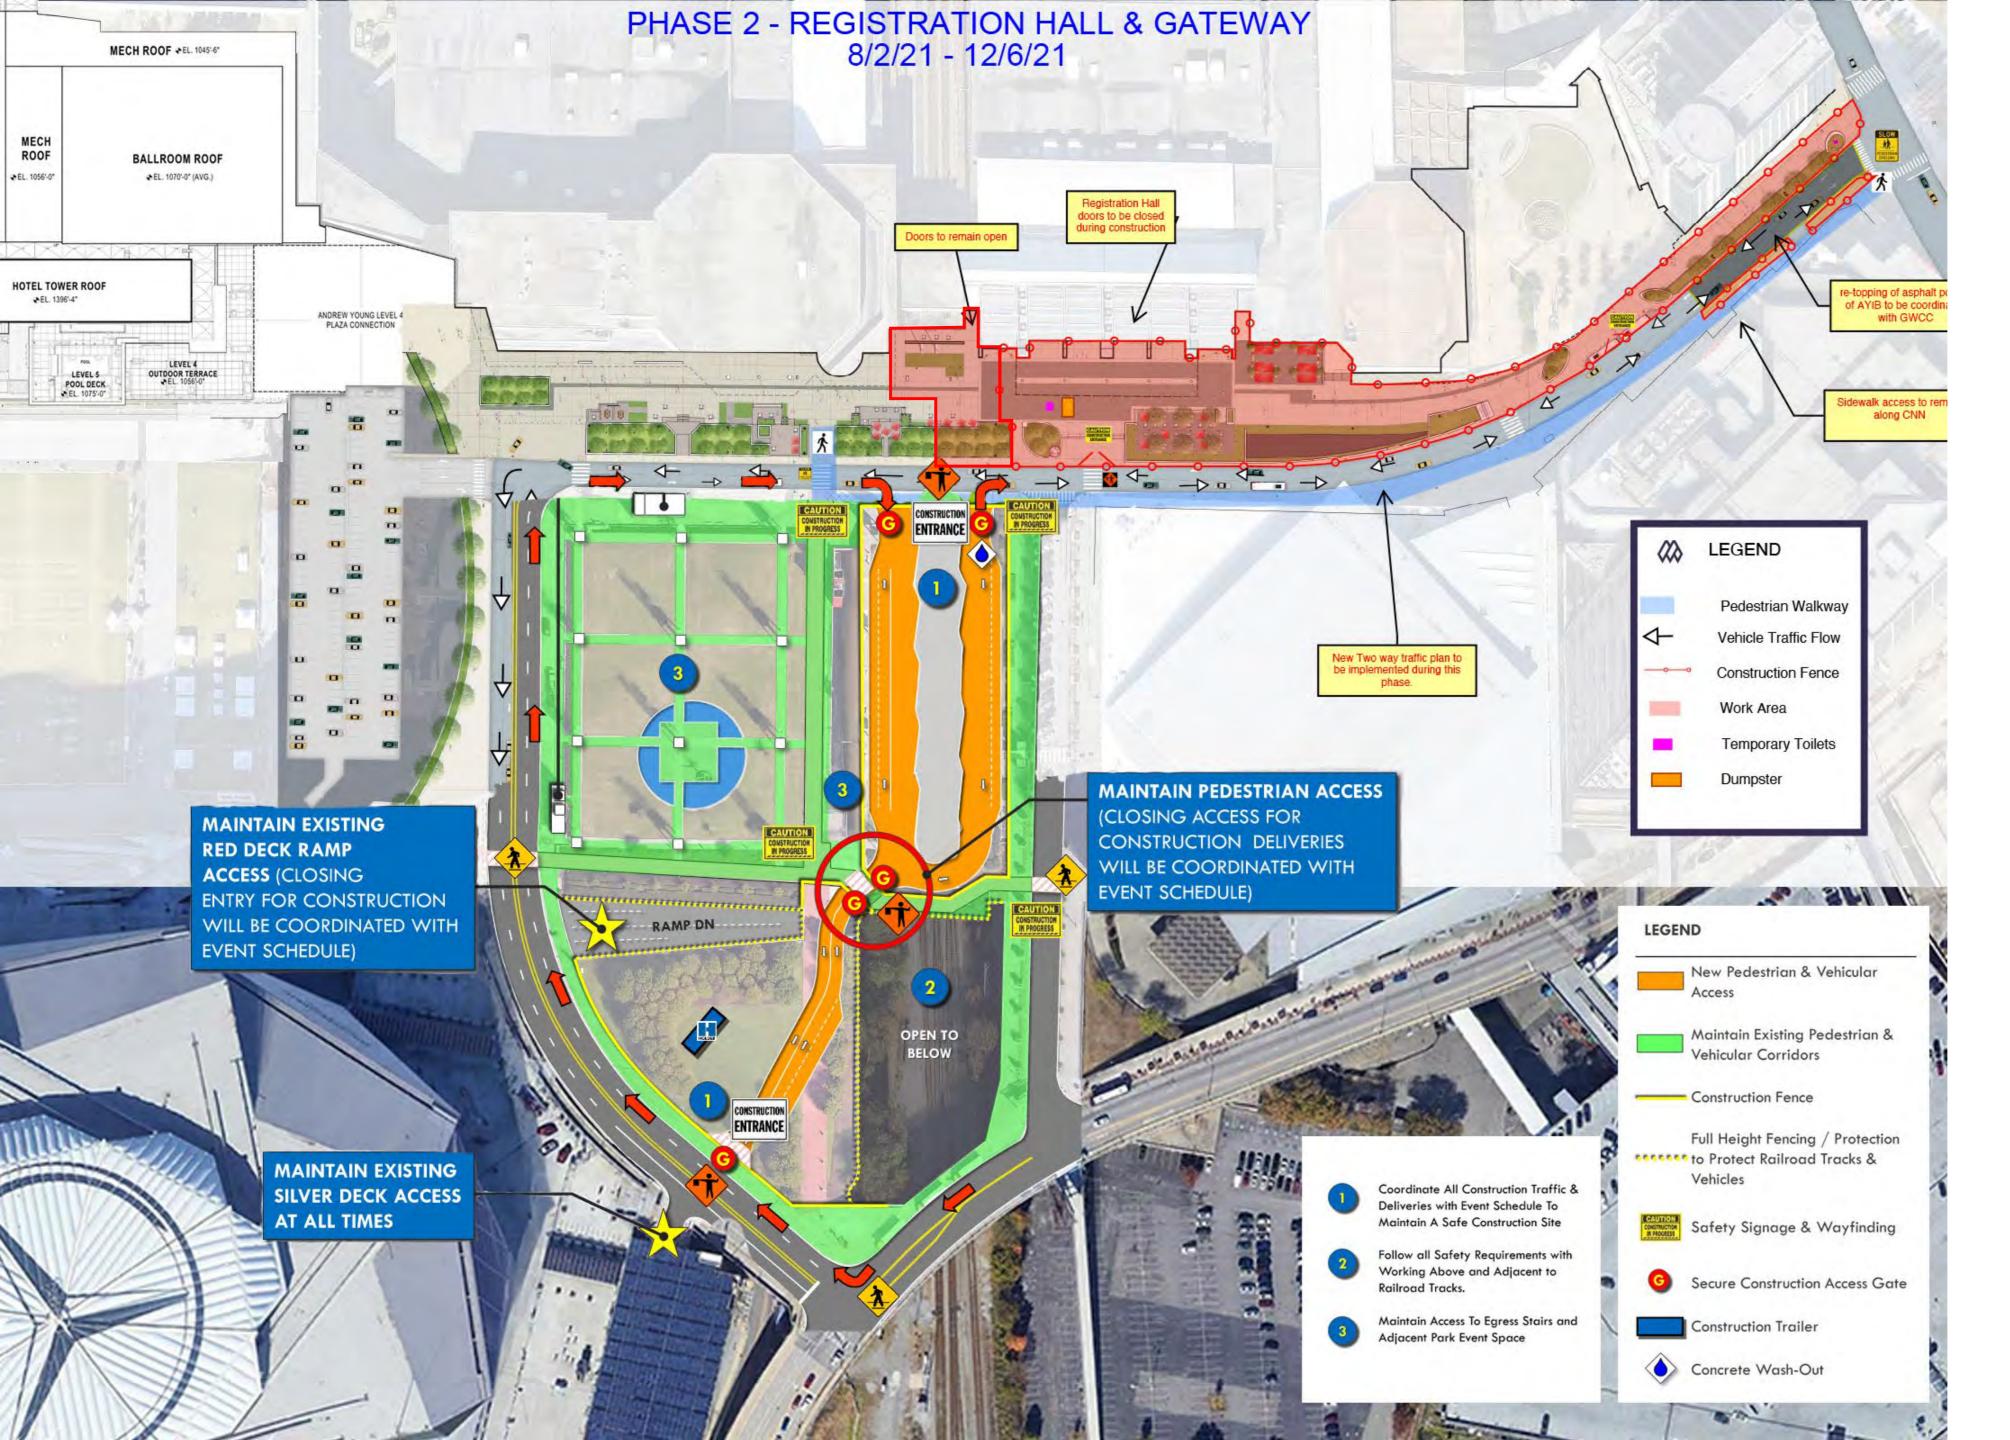

Pedestrian Mall
Phase 2
8/2/21 - 12/6/21

Transportation Depot 4/6/21 - 4/5/22


4-Week Look-Ahead Schedule - Pedestrian Mall



Area	Activity	Start Date	Finish Date
Phase 1	Waterproofing at Planters	5/10/21	7/27/21
	Irrigation Rough-in	5/18/21	7/27/21
	Install Deck Areas	5/20/21	7/13/21
	Soil at Planters	6/10/21	7/22/21
	Set Paver Pedestals	6/15/21	7/23/21
	Traffic Coating	6/17/21	7/26/21
	Install Expansion Joint at Roadway	6/17/21	7/12/21
	Install Pavers	6/18/21	7/16/21
	Deck Area Planter Curbs	6/23/21	7/15/21
	Demo/Replace Speed Humps/Crosswalks	6/28/21	7/16/21
	Form ADA Ramps at Crosswalks	7/7/21	7/13/21
	1" Sidewalk Topping	7/7/21	7/27/21
	Light Poles	7/9/21	7/22/21
	Steel for Green Walls at Decks	7/13/21	7/26/21
	Signage Relocation	7/16/21	7/19/21
	Stone 1 st Delivery and Install	7/19/21	7/28/21
	Stone 2 nd Delivery and Install	7/26/21	8/11/21
	Event Prep/Fence Reconfiguration/Staging	7/27/21	7/28/21


Pedestrian Mall – Phase 1 Completion Plan



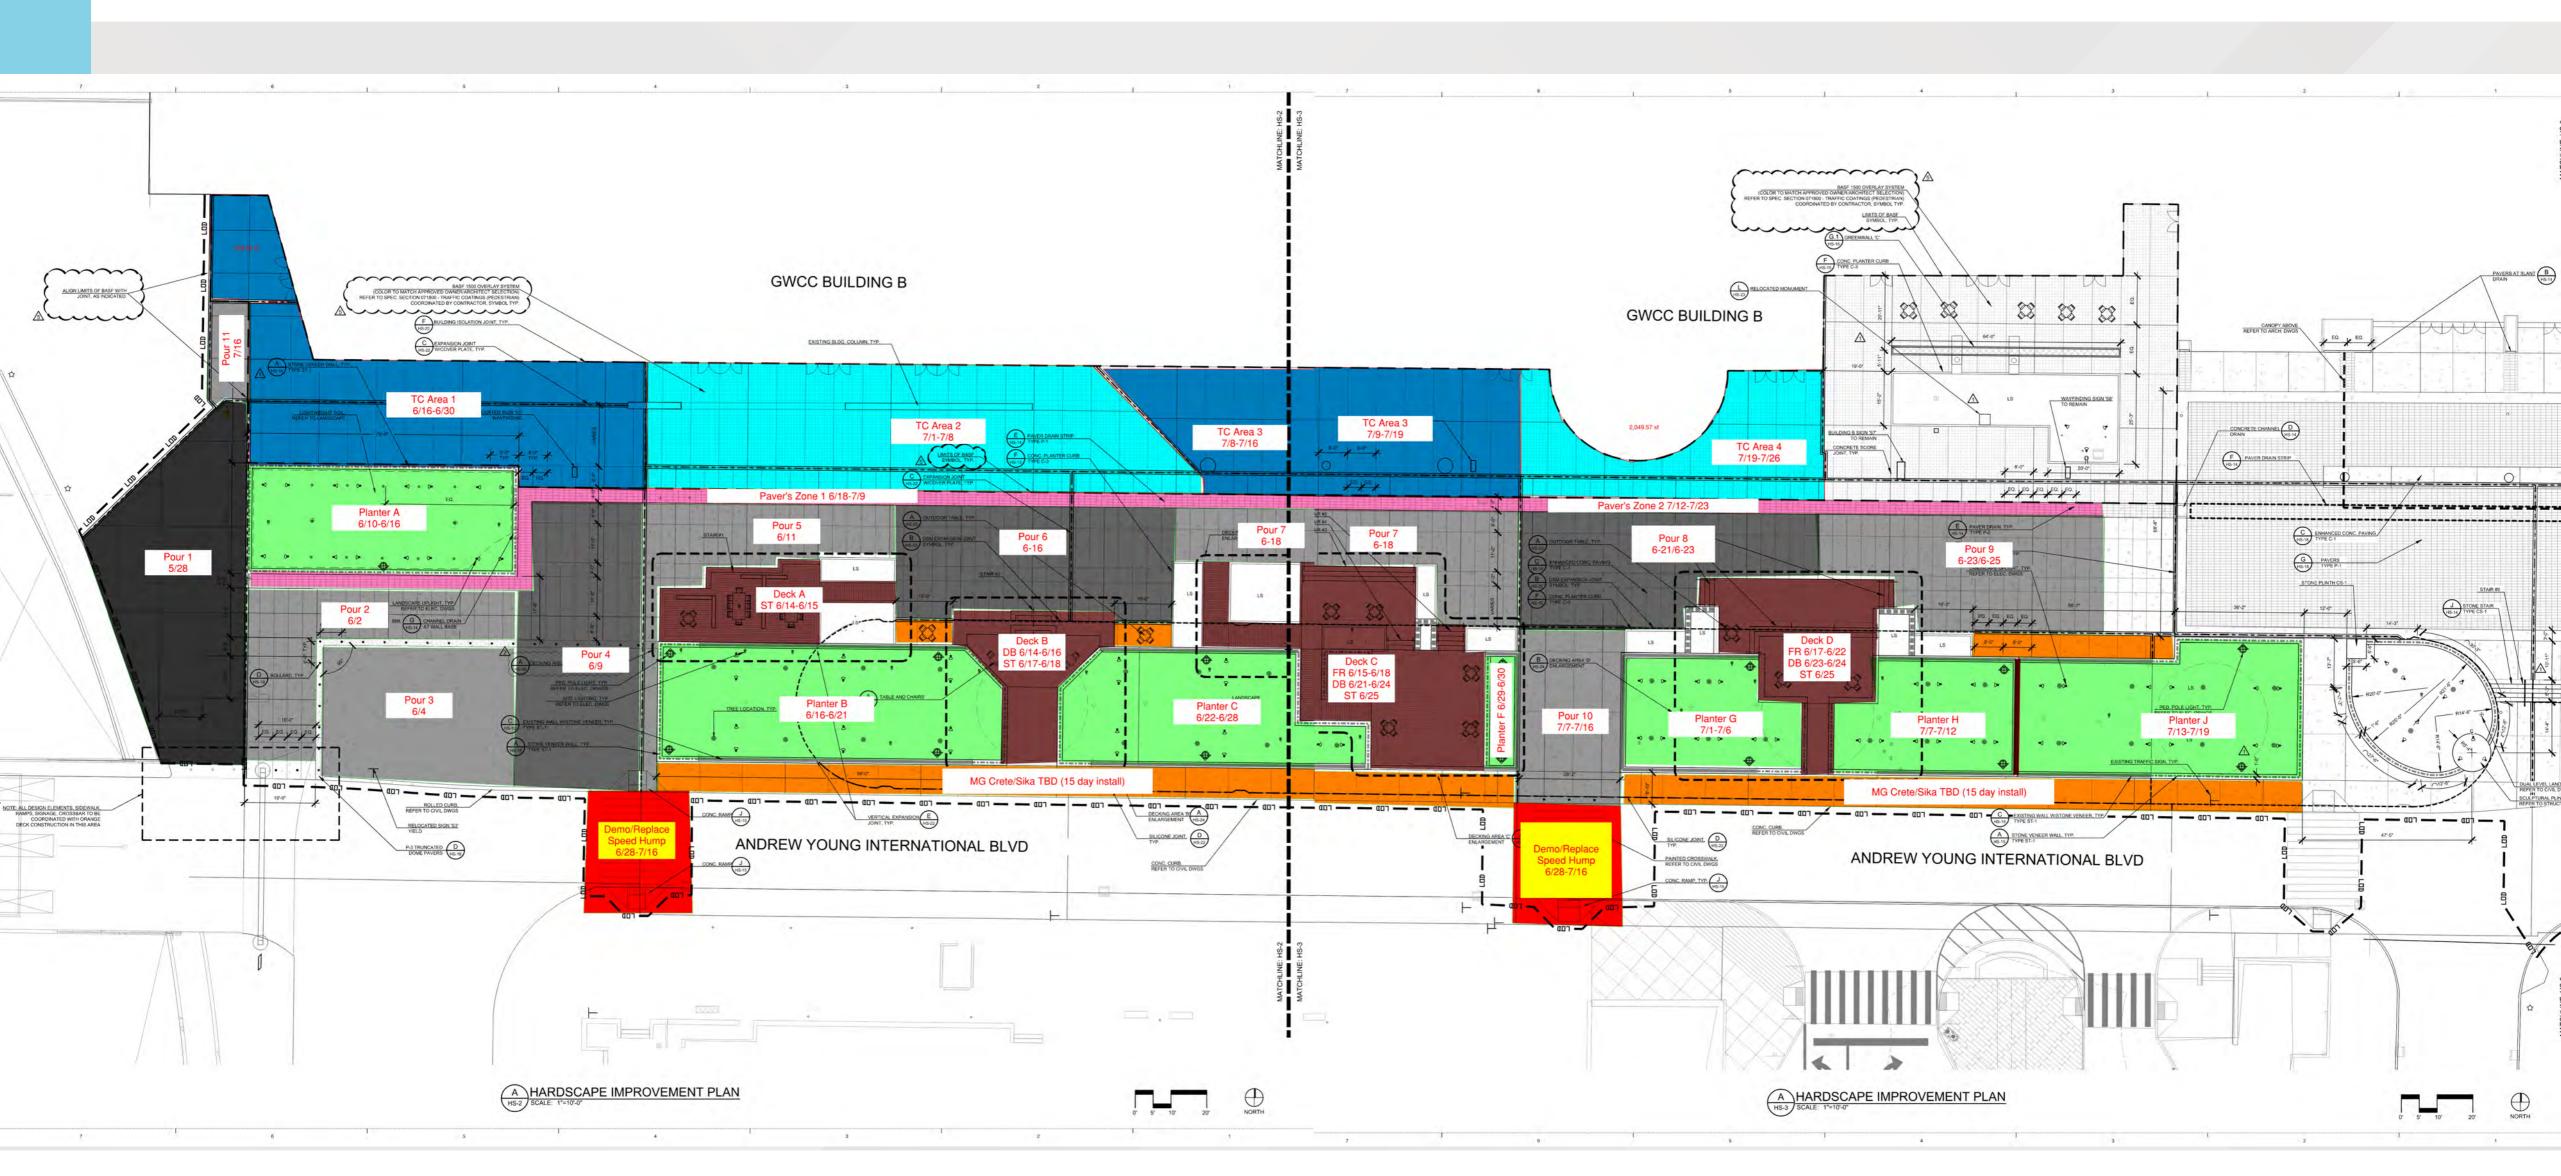

Pedestrian Mall – Phase 1 Stone Installation Plan



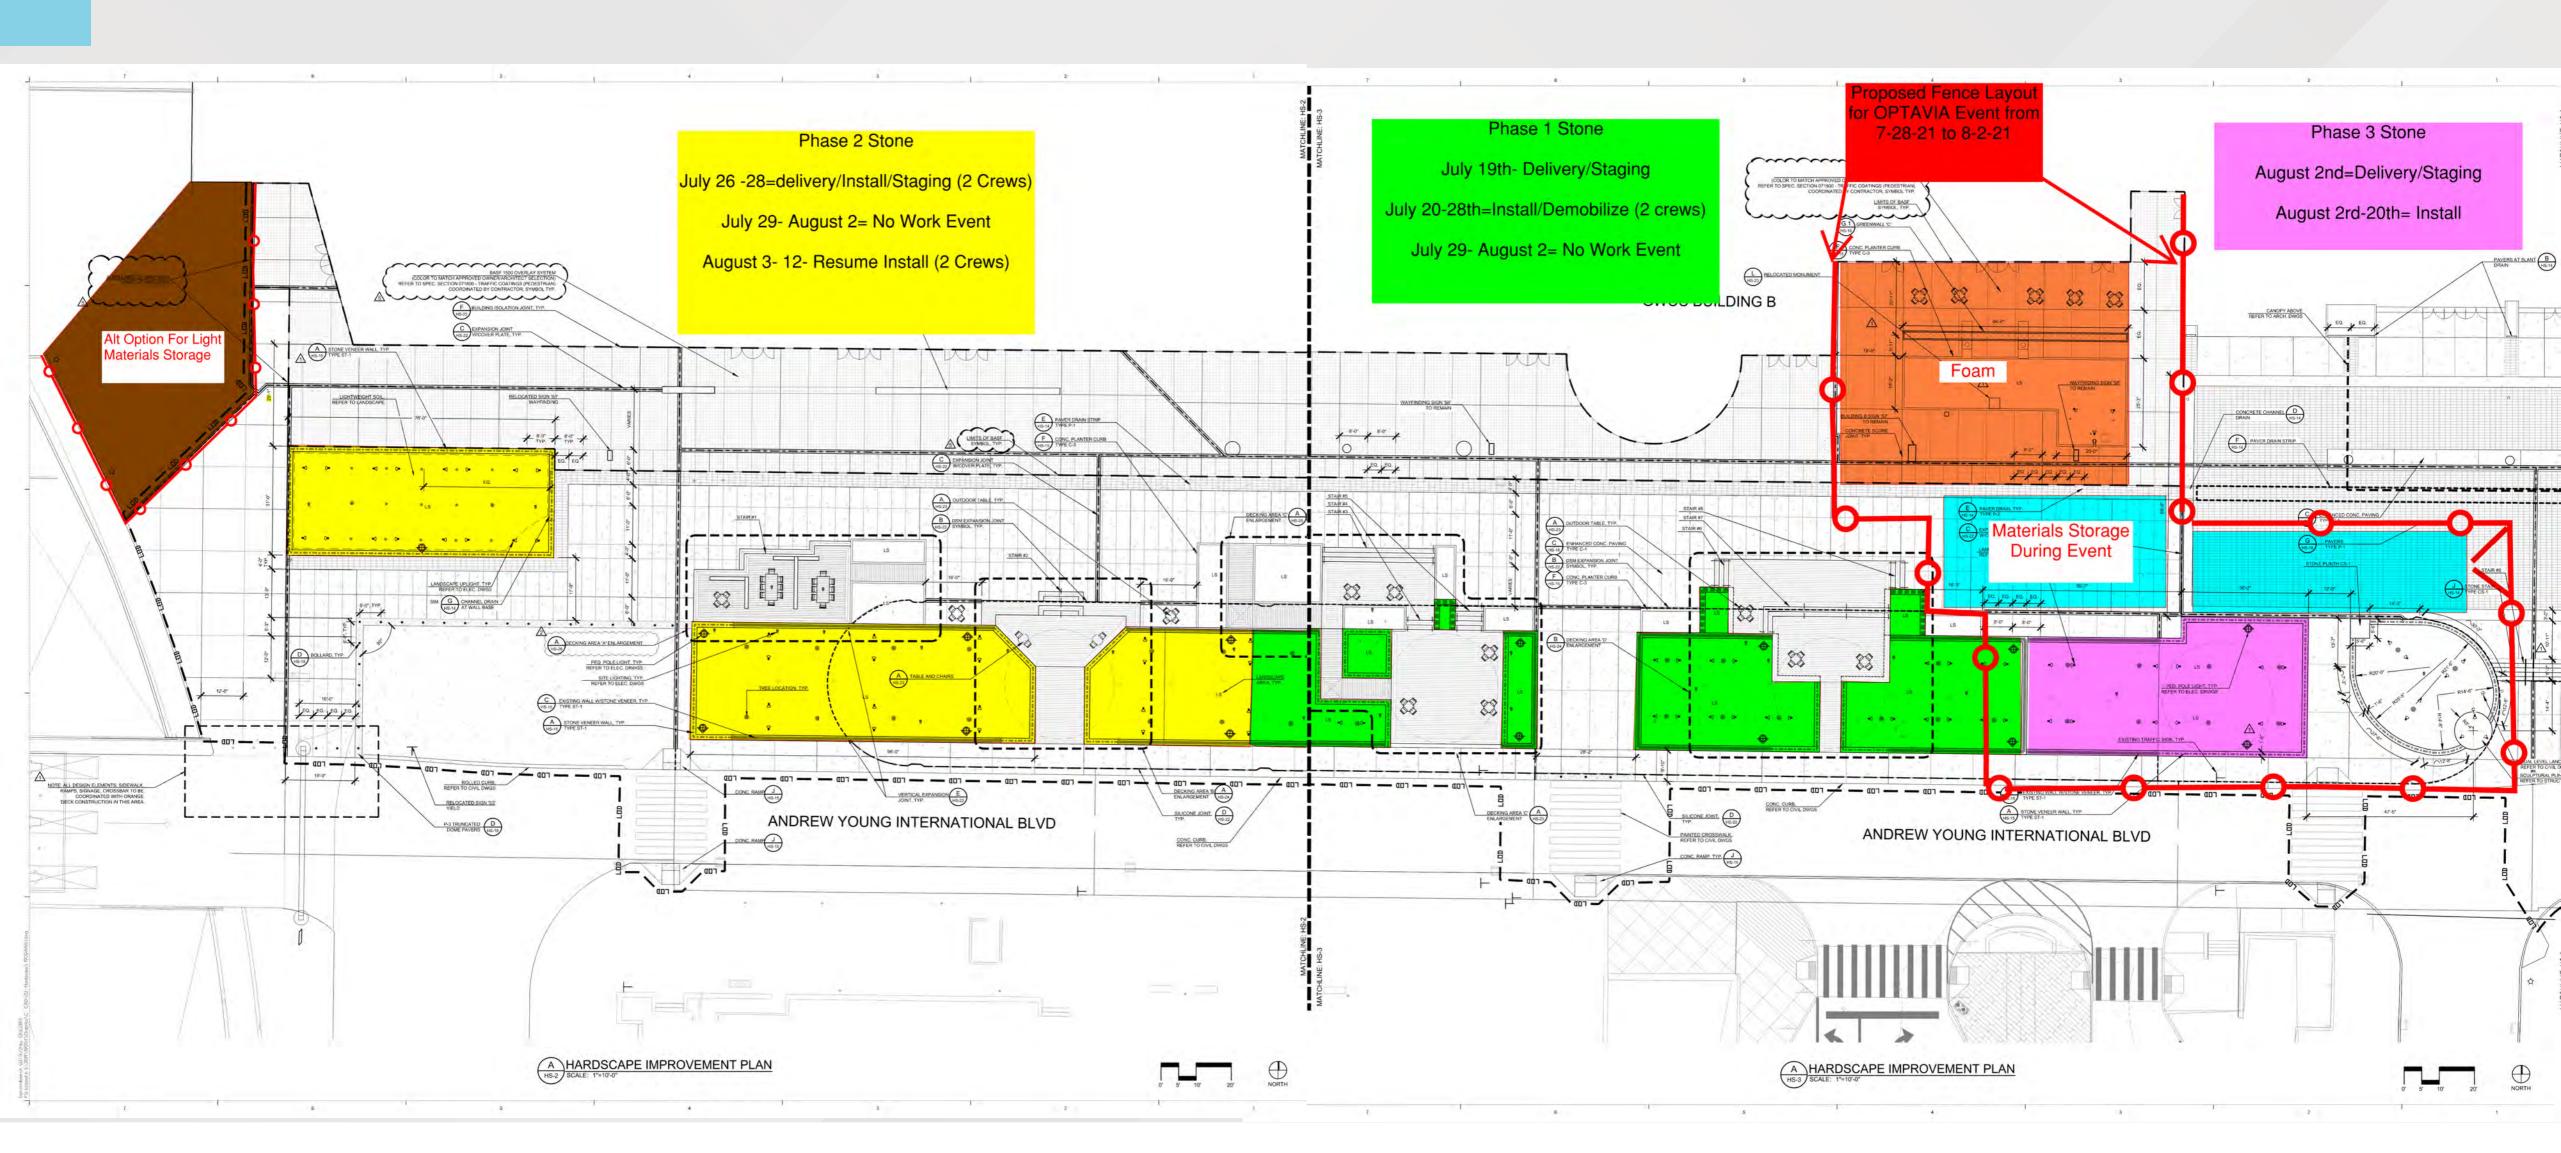






Pedestrian Mall July 7 Photos







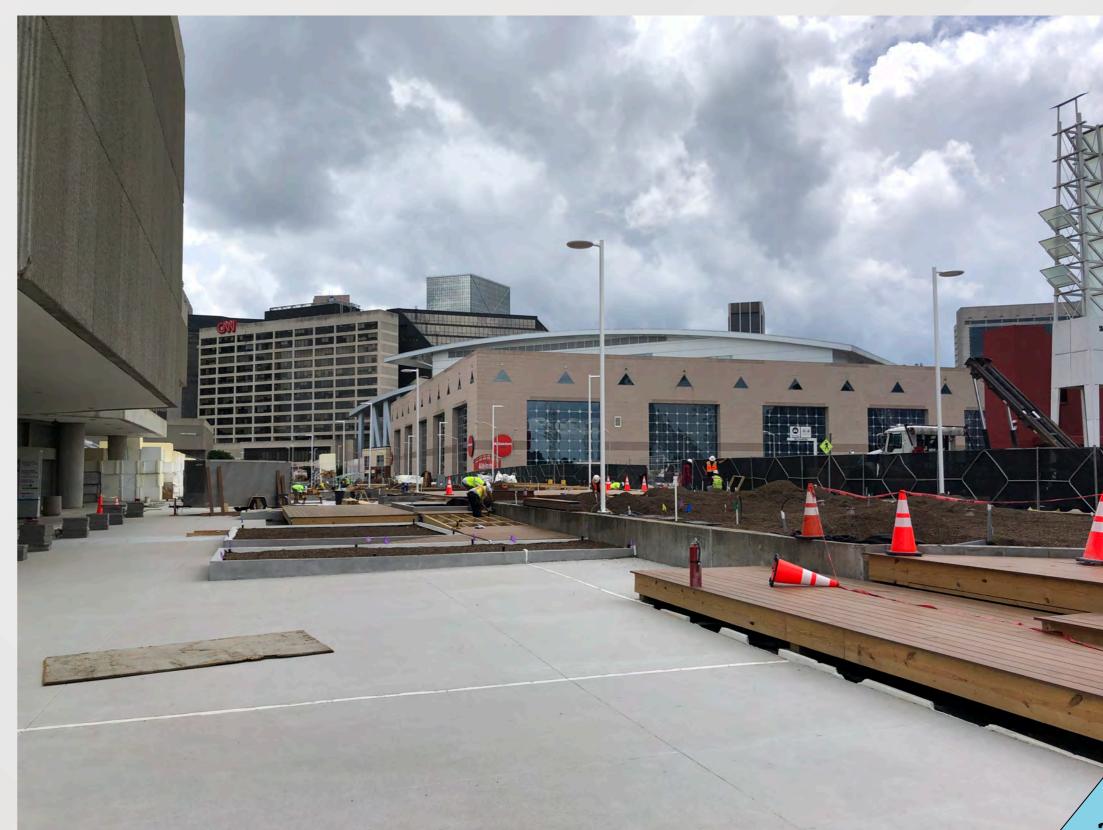


Pedestrian Mall June 23 Photos



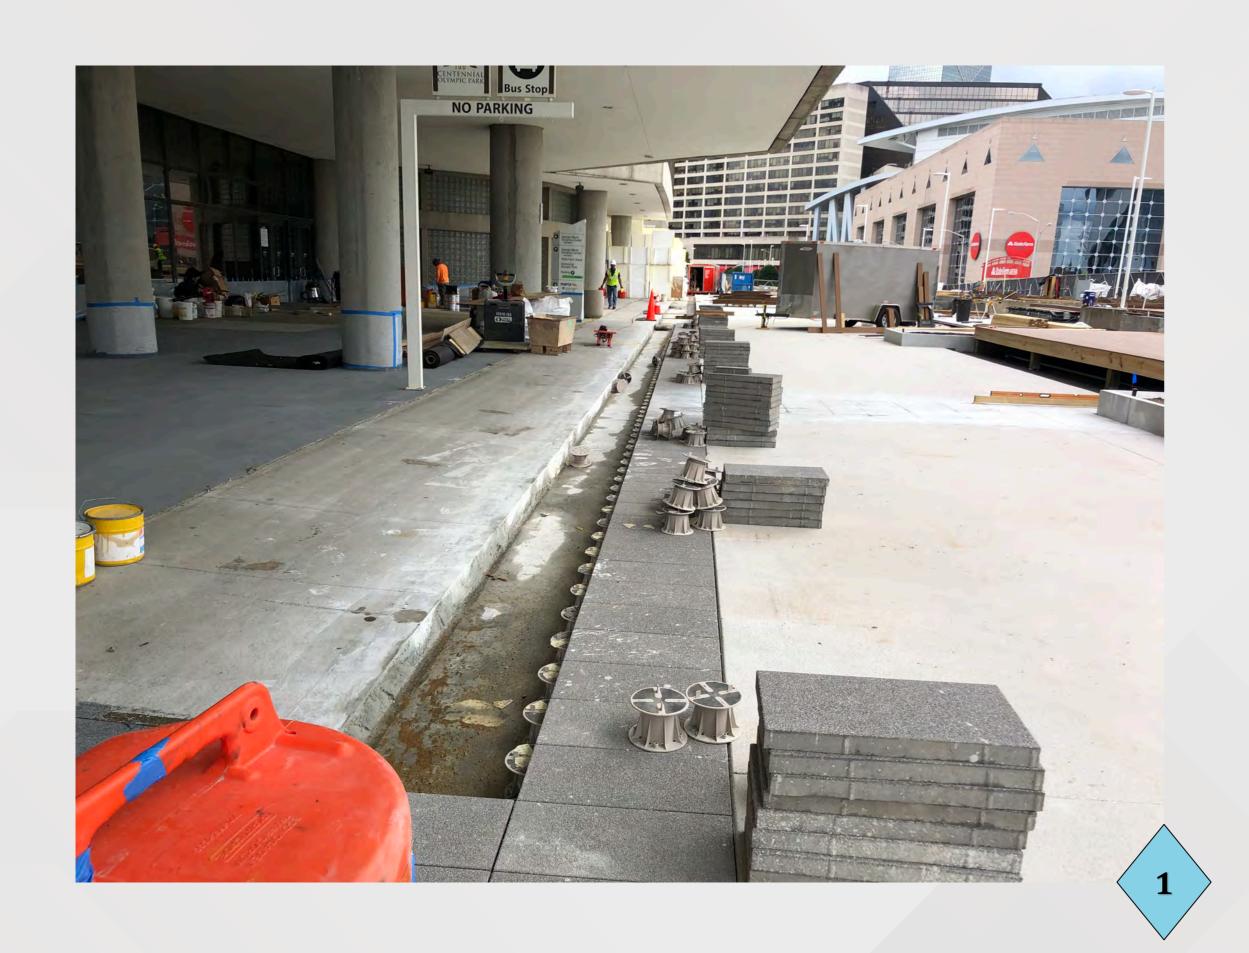


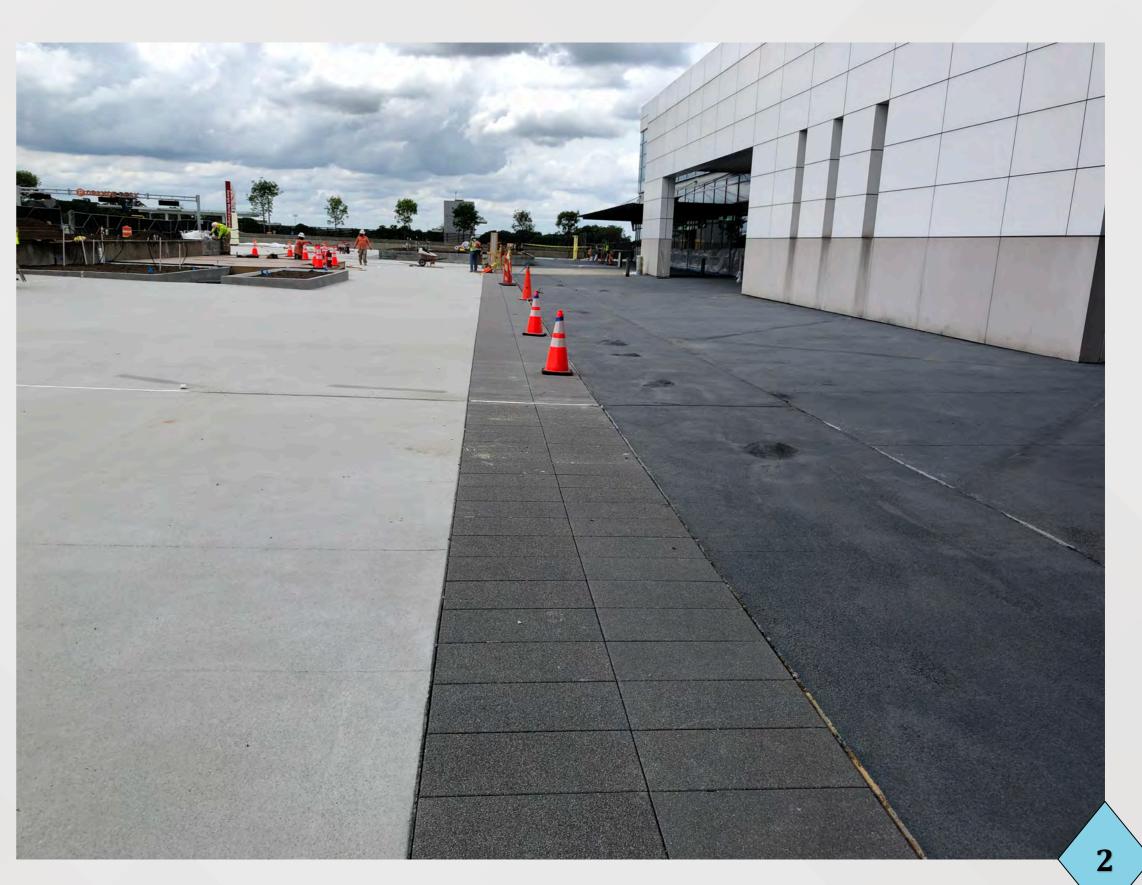


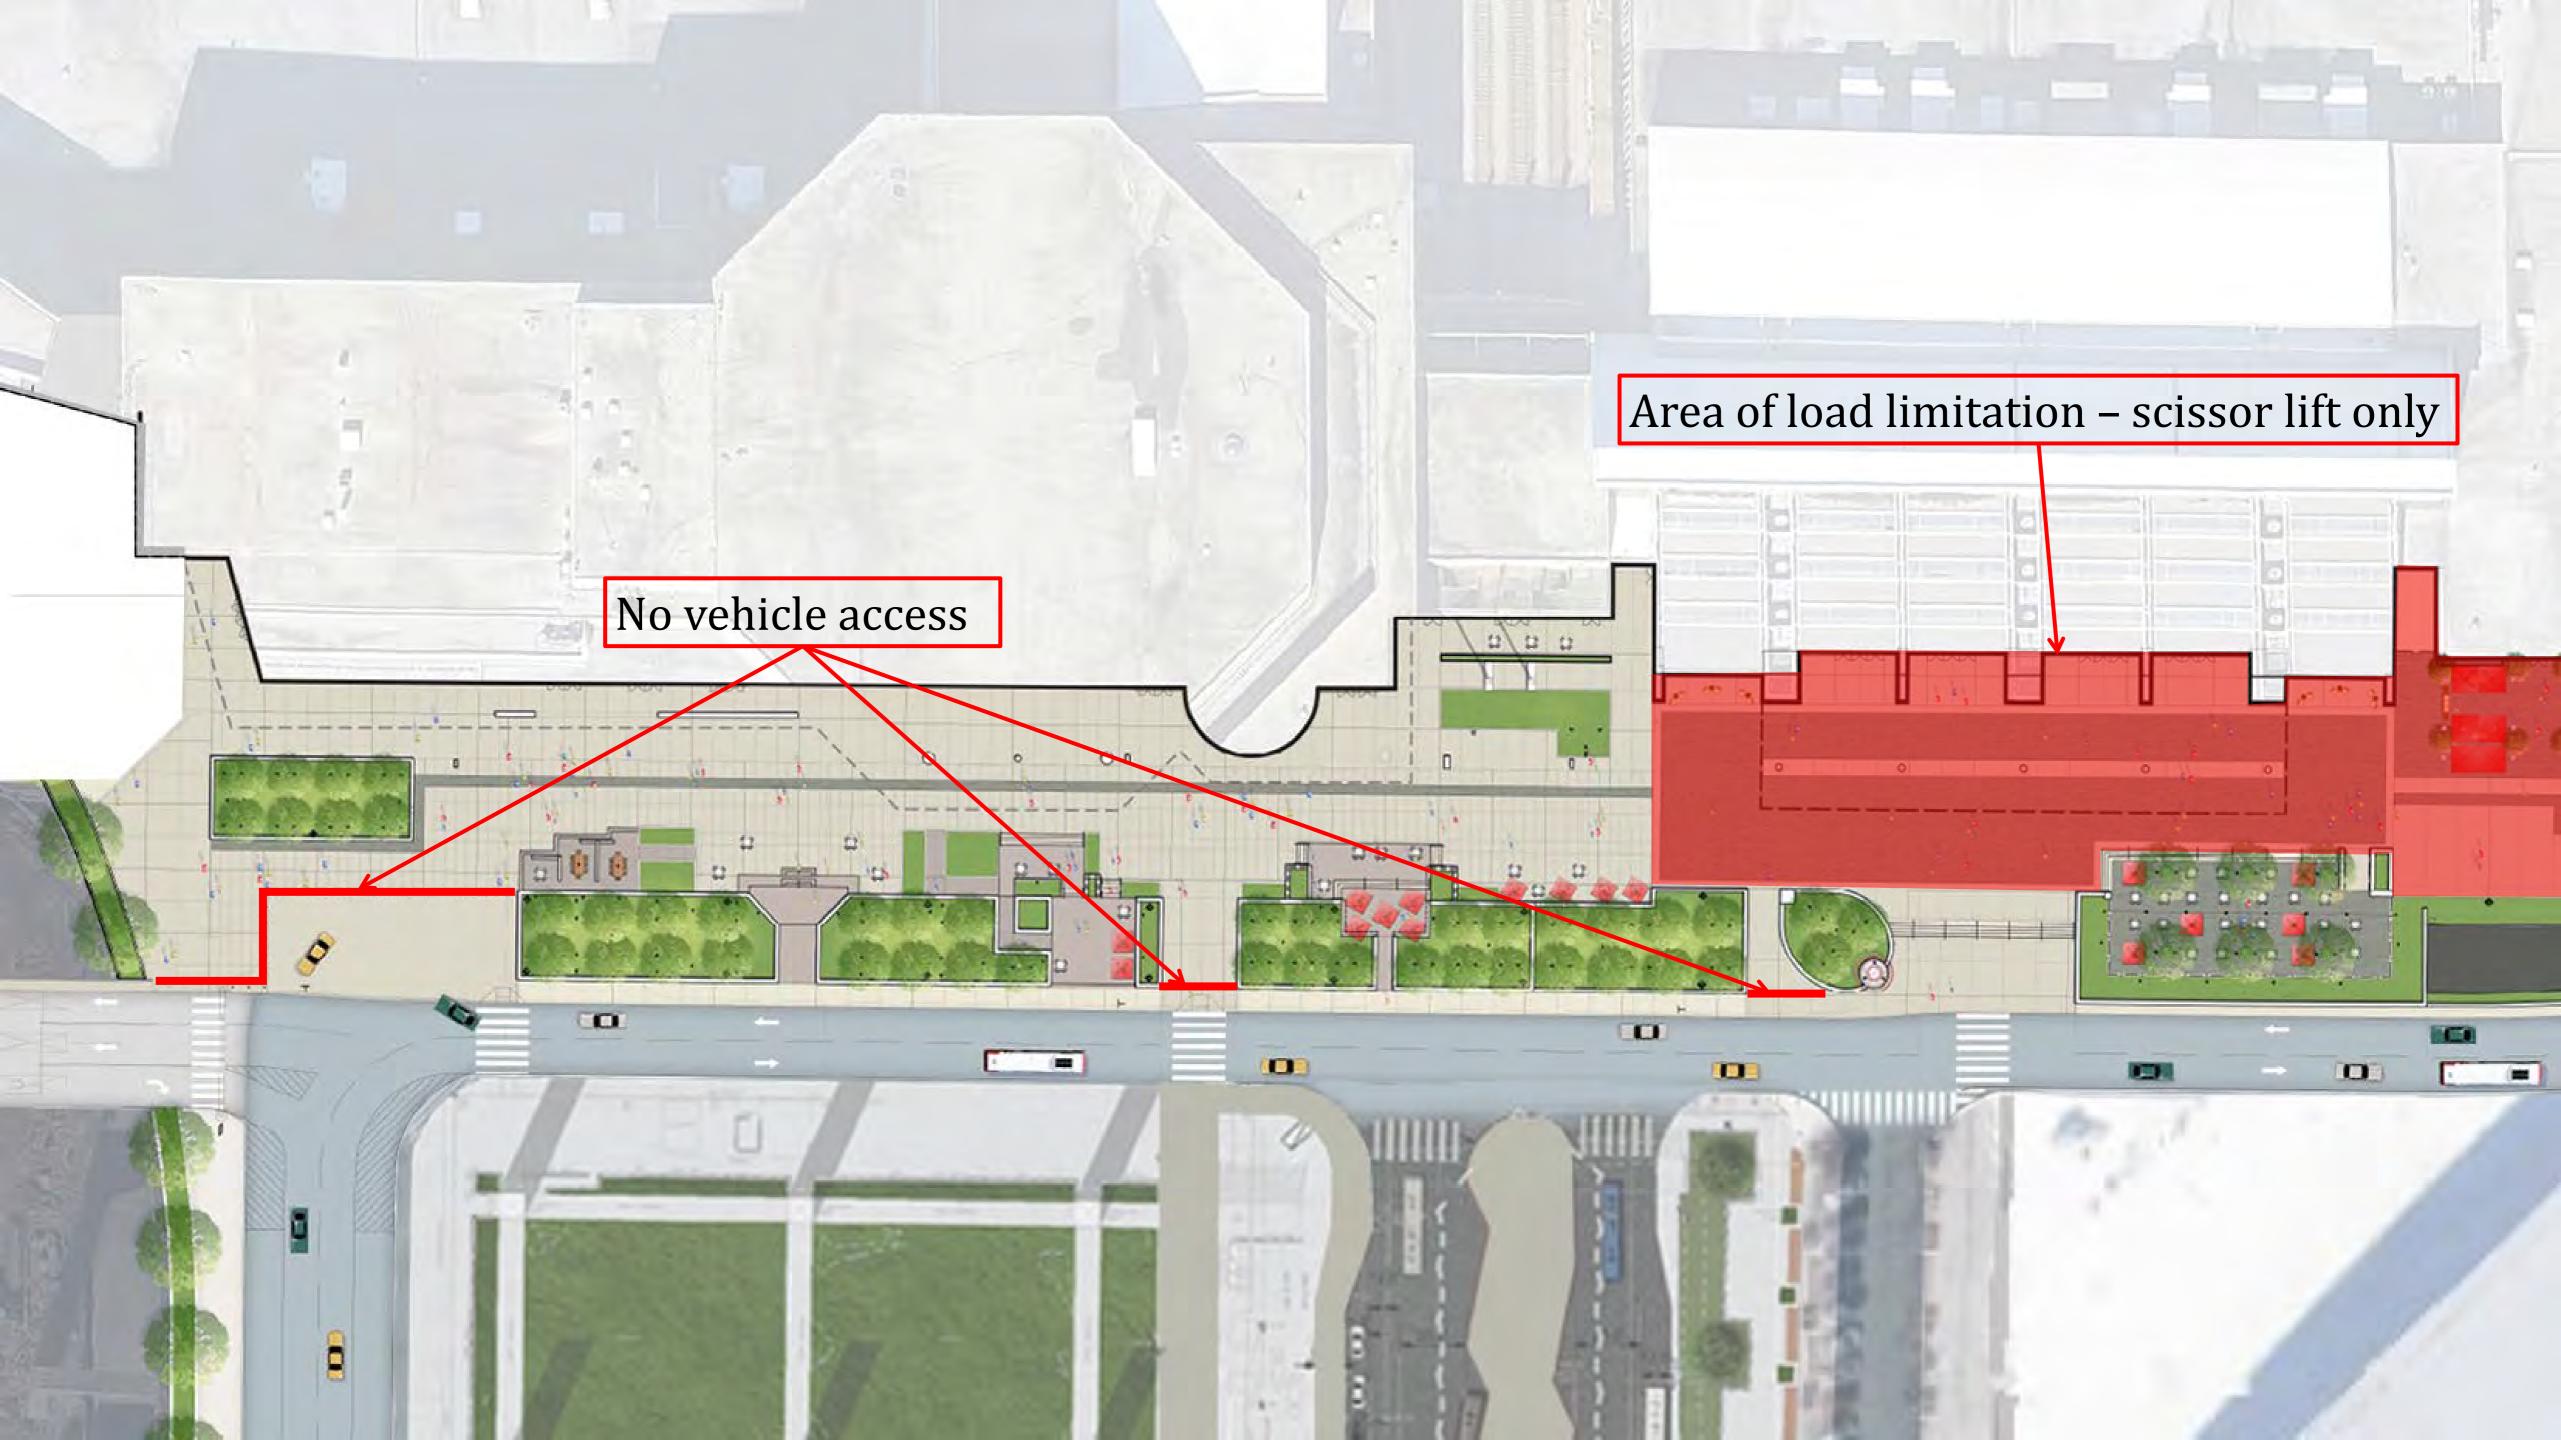

Pedestrian Mall June 23 Photos




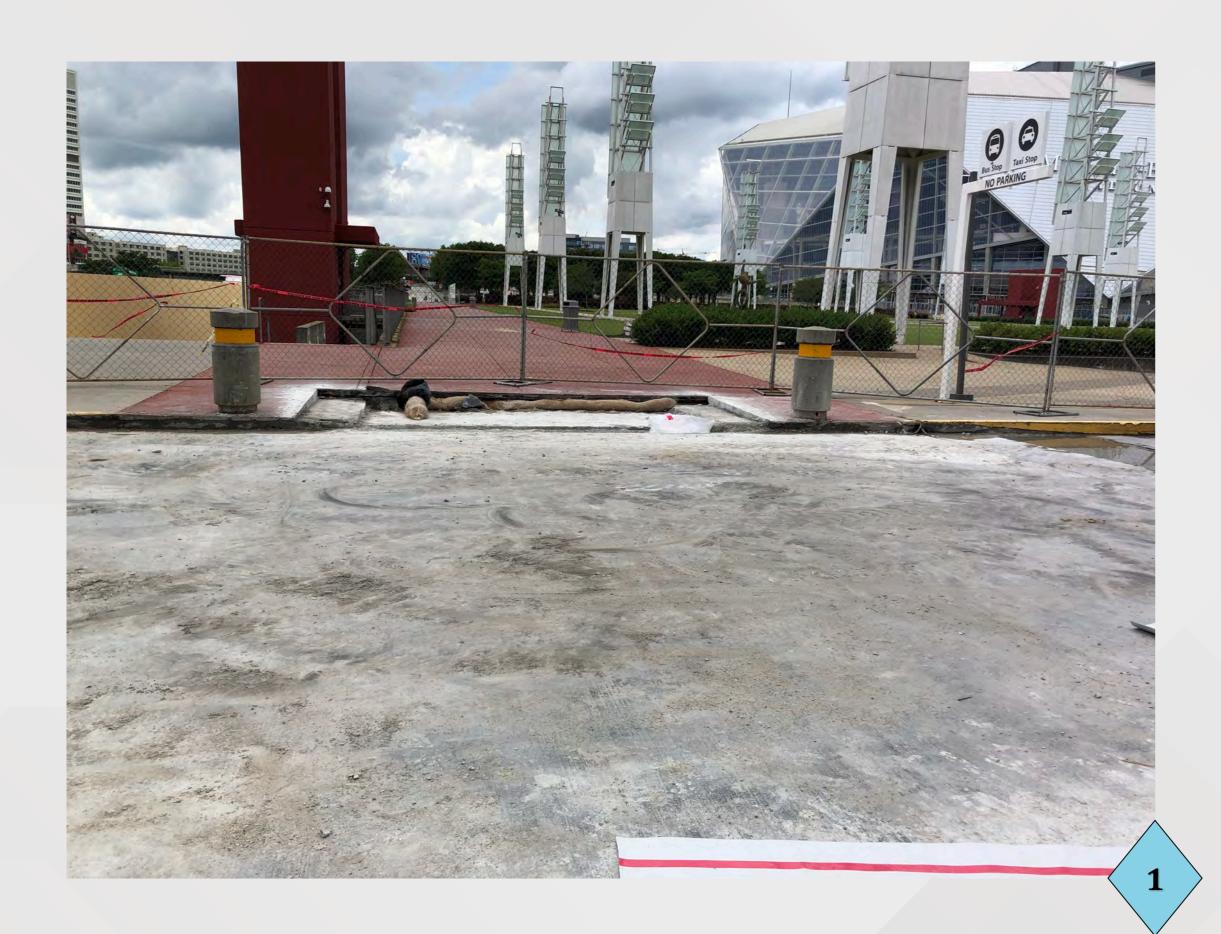

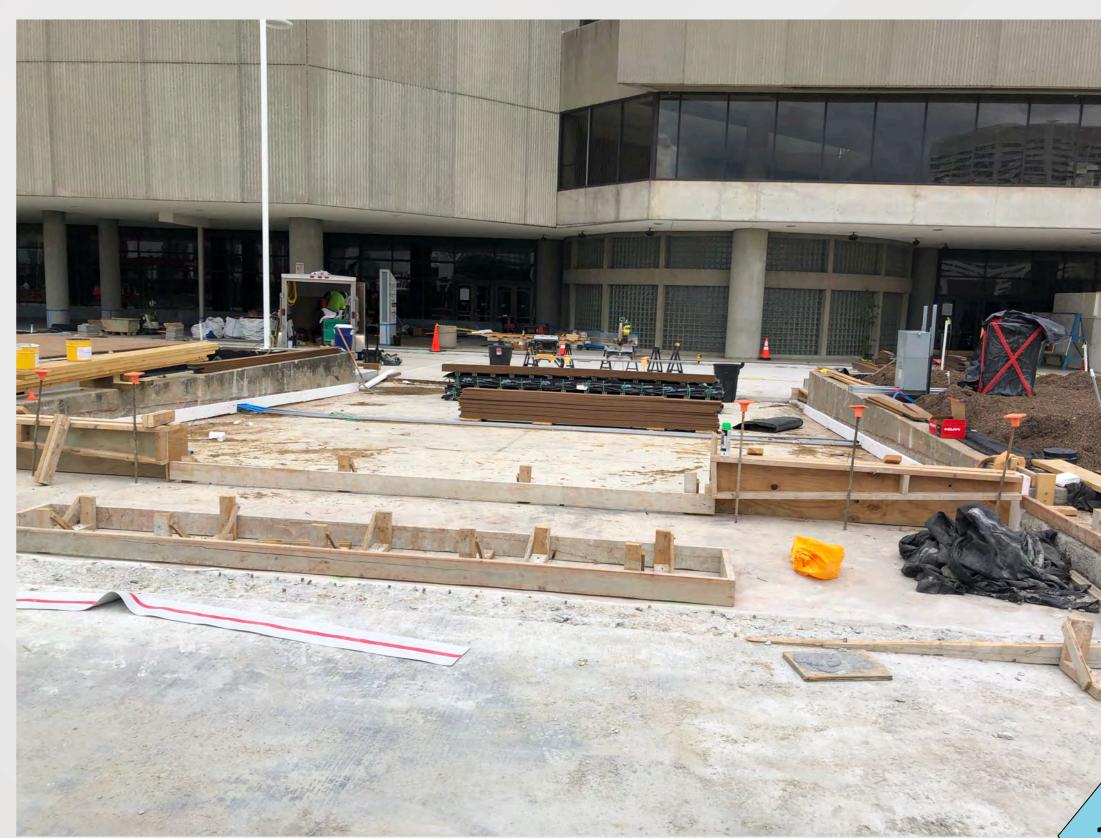

Pedestrian Mall June 23 Photos



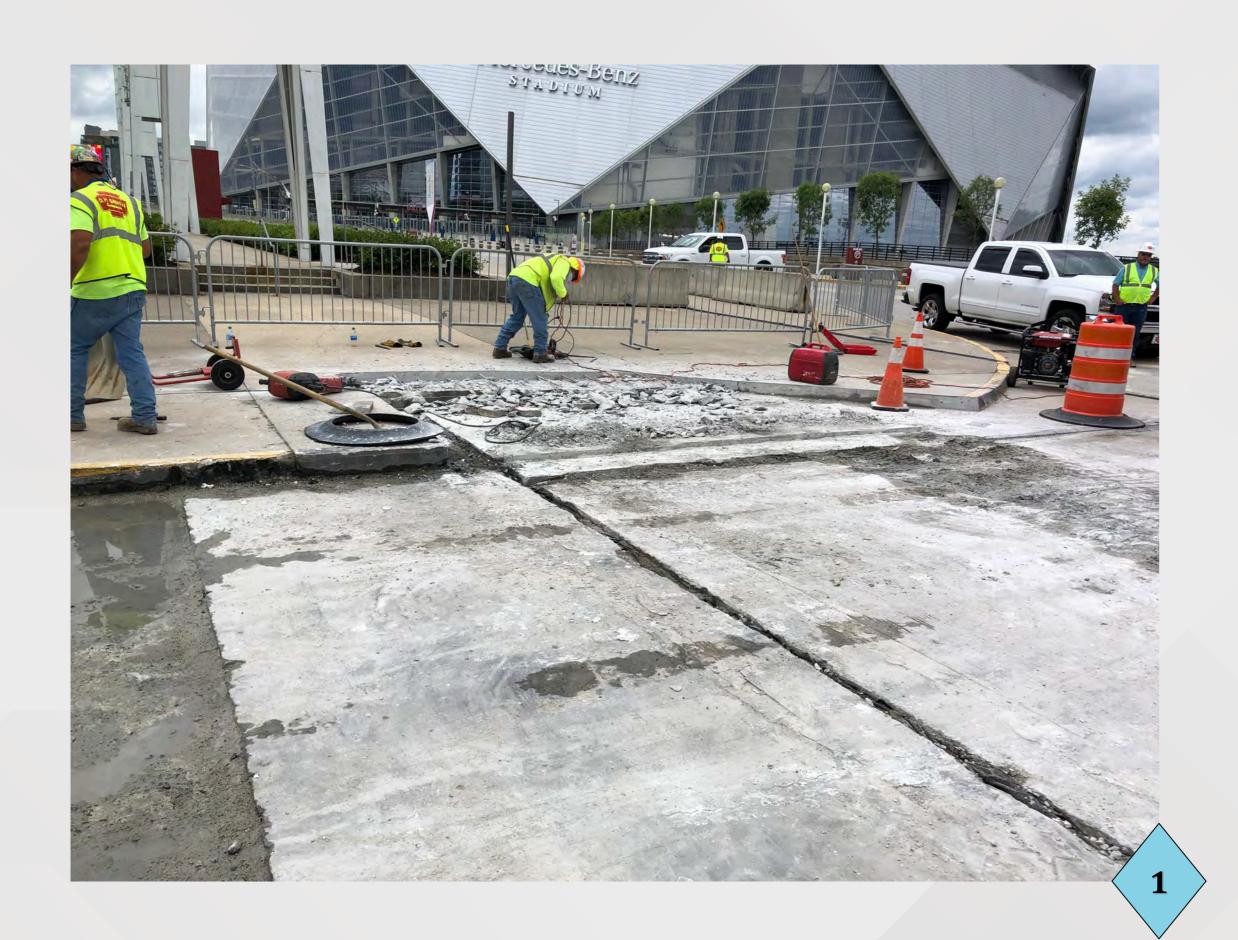




4-Week Look-Ahead Schedule – Transportation Depot




Area	Activity	Start Date	Finish Date
Depot Area	Structural Concrete Pour 1	5/10/21	7/26/21
	Structural Concrete Pour 2	5/27/21	8/10/21
	Structural Concrete Pour 3	6/11/21	8/20/21
	Structural Concrete Pour 4	6/24/21	9/1/21
Bridge Area	F/R/P Pile Cap Concrete Cure Time	6/17/21	7/16/21
	Erect Steel Support Beams	8/5/21	8/18/21
Red Deck Area	Hang New Electrical Panel	7/1/21	7/2/21
	Overhead Conduit to Depot for Power, AV, LV	7/6/21	8/2/21
South Drive Area	Structural Improvements	5/19/21	10/13/21
	Zone A Rods Material Delivery	6/15/21	7/6/21
	Zone A Drop Rods	7/7/21	7/20/21
	Zone A Install Angles	7/14/21	8/3/21
	Zone B Layout & Drill for Rods	6/16/21	7/7/21
	Zone B Drop Rods	7/8/21	7/28/21
	Zone C Layout & Drill for Rods	6/25/21	7/9/21
	Zone C Drop Rods	7/22/21	8/4/21
	Zone D Layout & Drill for Rods	7/12/21	7/30/21
	Zone D Drop Rods	7/29/21	8/11/21

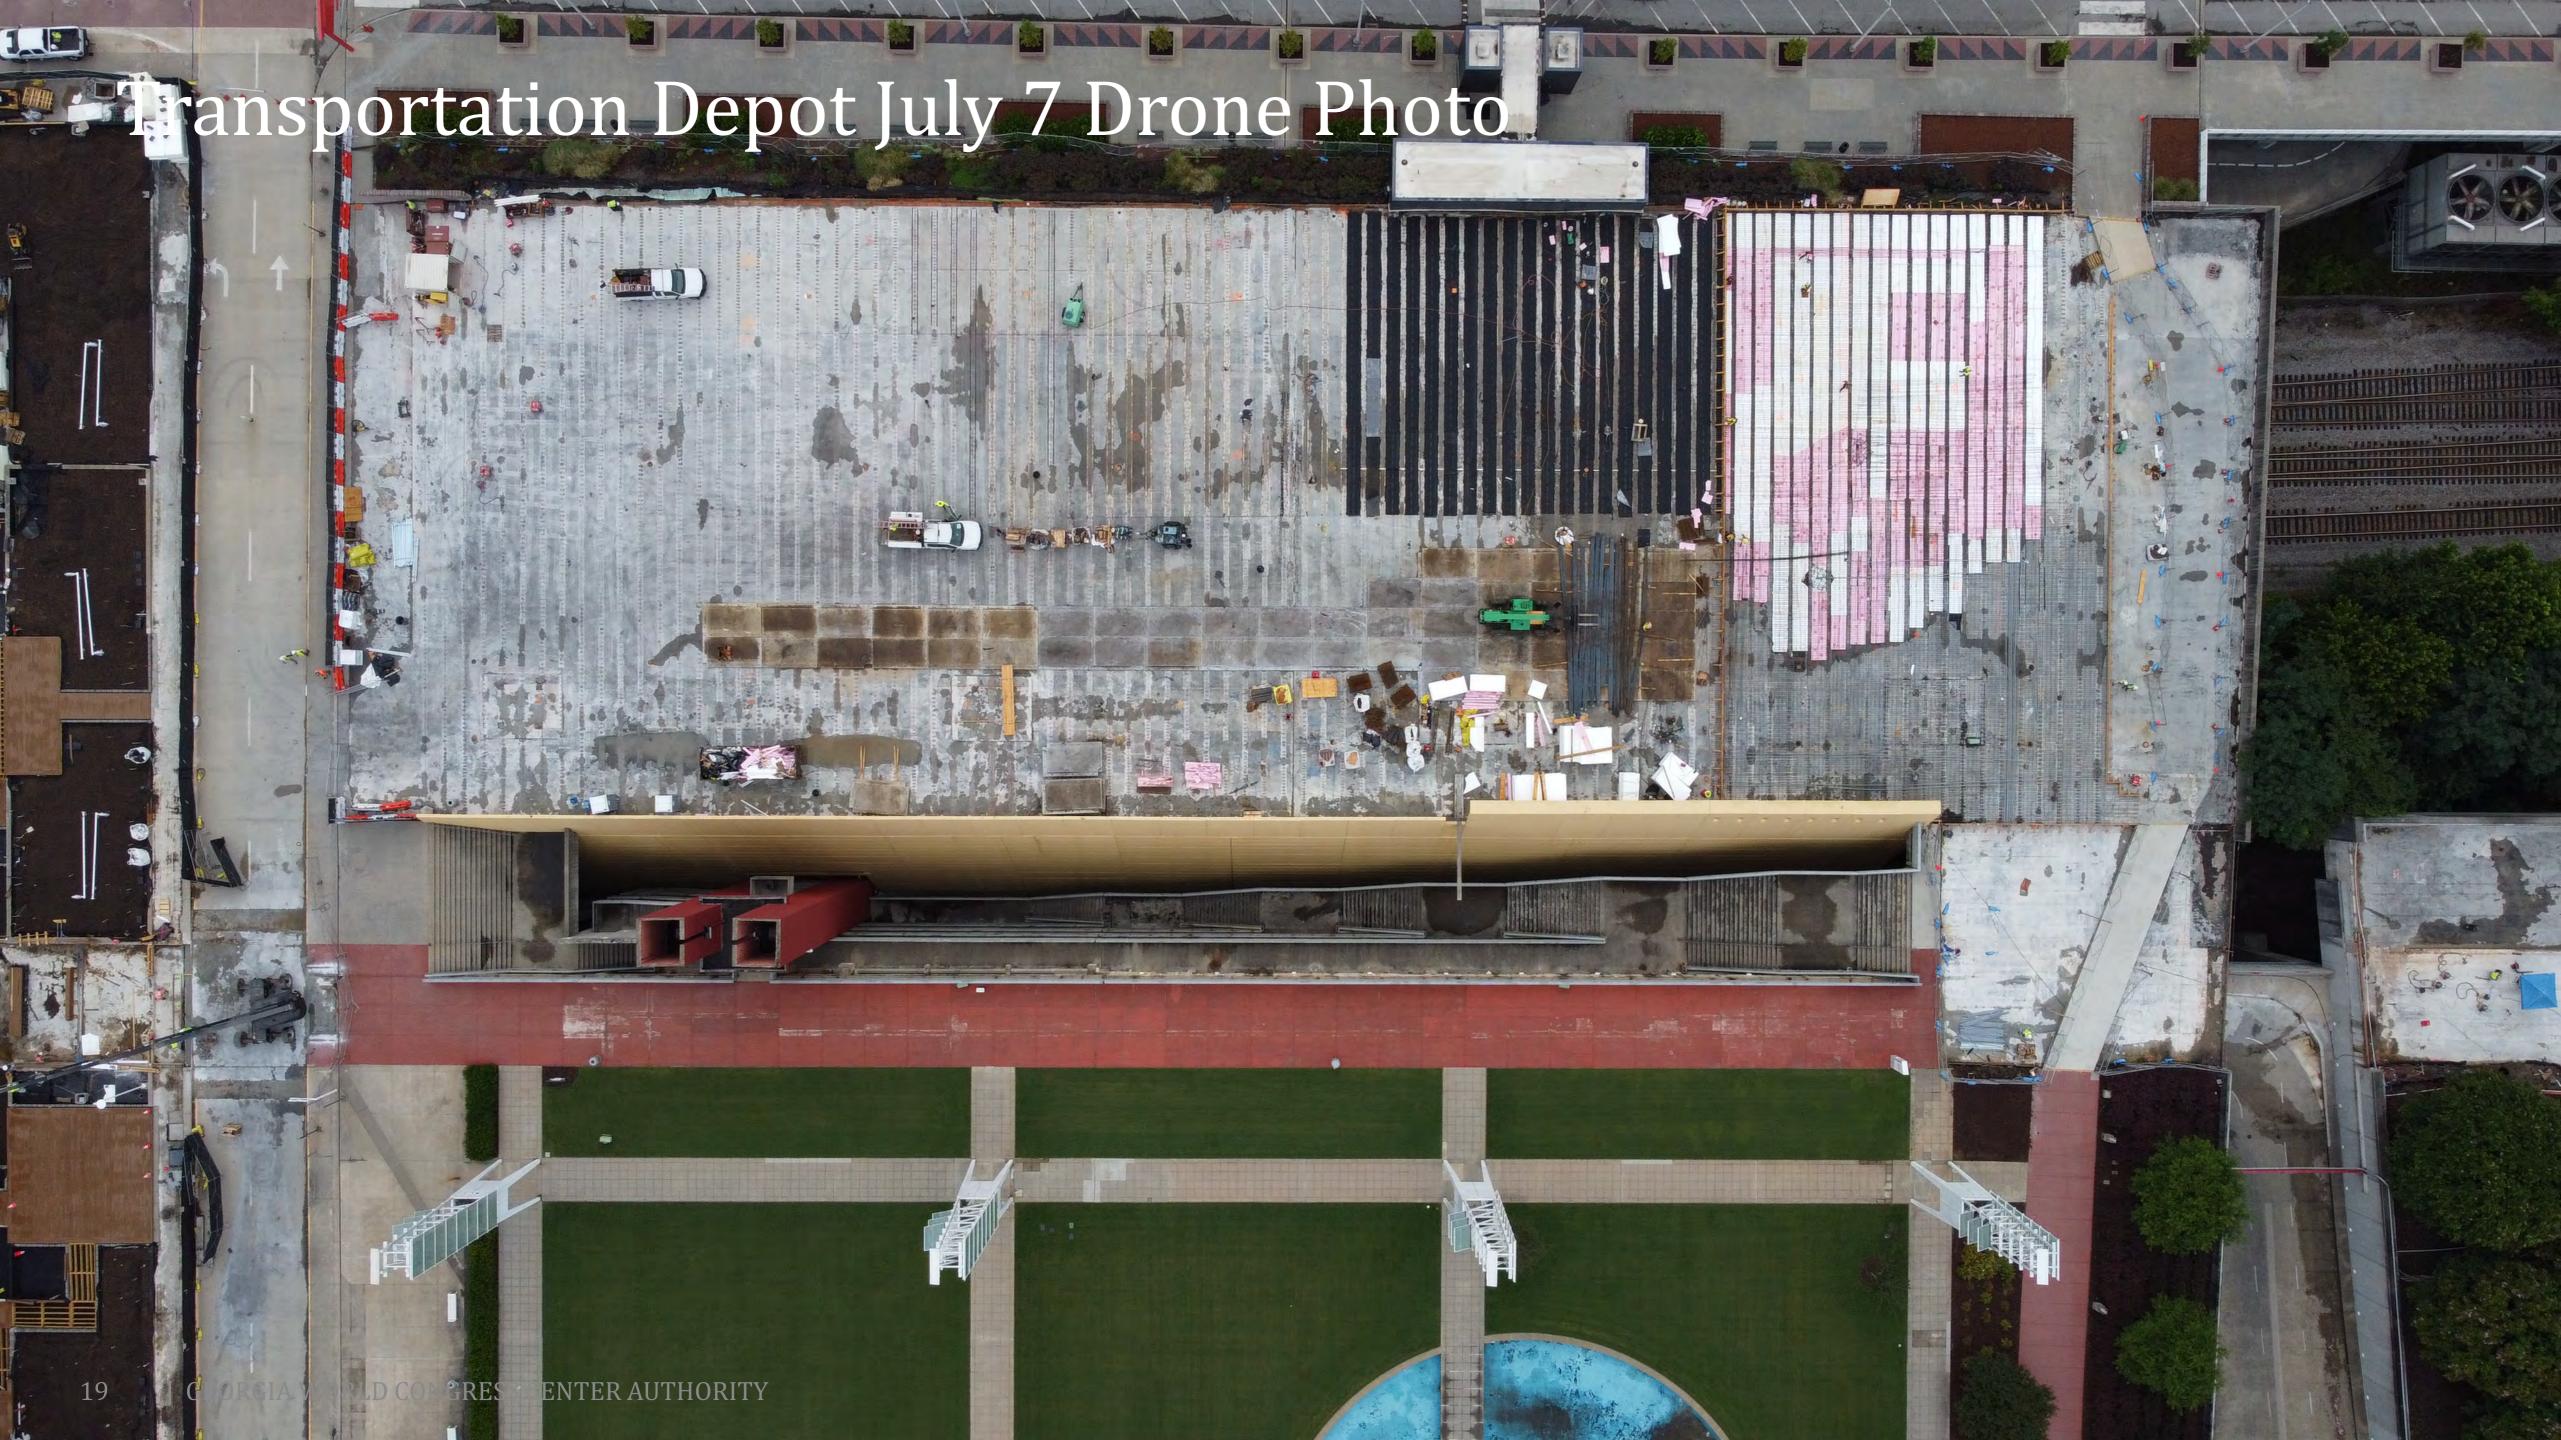




Transportation Depot June 23 Photos




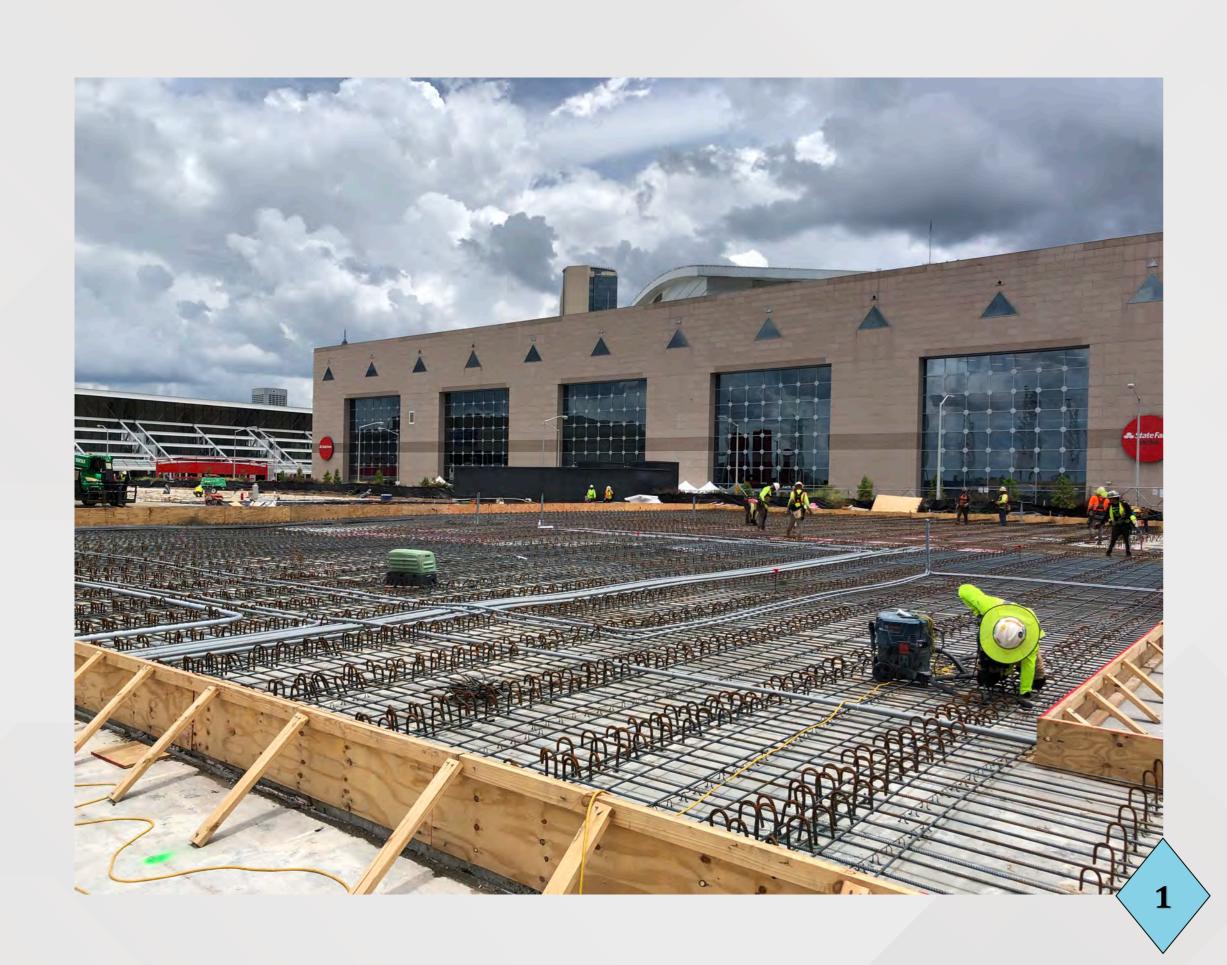

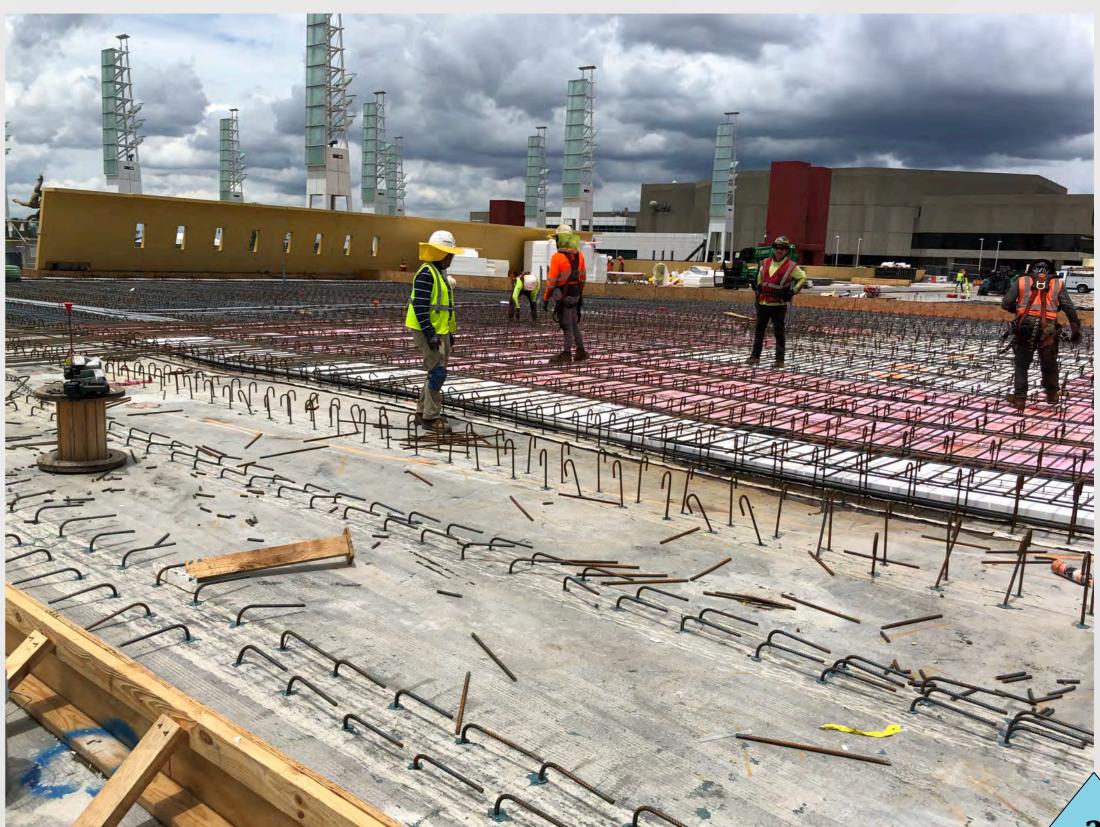

Transportation Depot June 23 Photos



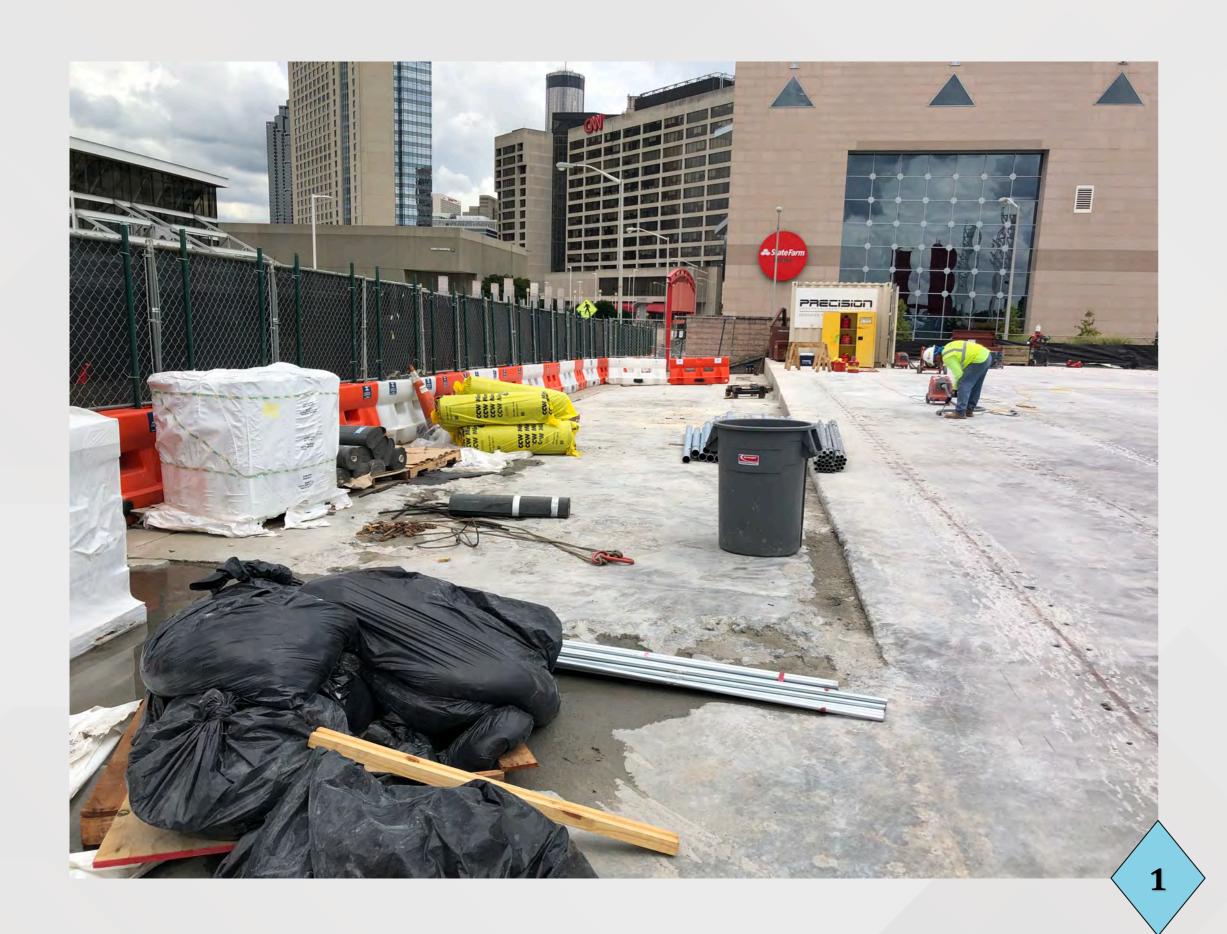





Project Information

- Project Manager: Ken Stockdell
- Project Scope: Replacing sections of roof on Buildings A & B classified as in need of "urgent" replacement status.
- Project Location: Sections of Building A & B Roofs

• Project Status

- Current Phase: Design Phase
- Proposed Construction Schedule
 - Design Phase: February 2021 June 2021
 - Preconstruction/Pricing Phase: June 2021 August 2021
 - Estimated Construction Phase: TBD

GWCCA "Urgent" Roof Replacement Areas



• Priority 1

- Exhibit Halls B4 & B5
- 6 Months

• Priority 2


- Main Lobby (Outside Reg Hall) & East Plaza Trayed Roofs
- 3 Months

• Priority 3

- Building A Level 4 Meeting Rooms
- 4 Months

• Priority 4

- Exhibit Hall A1-A3
- 6 Months

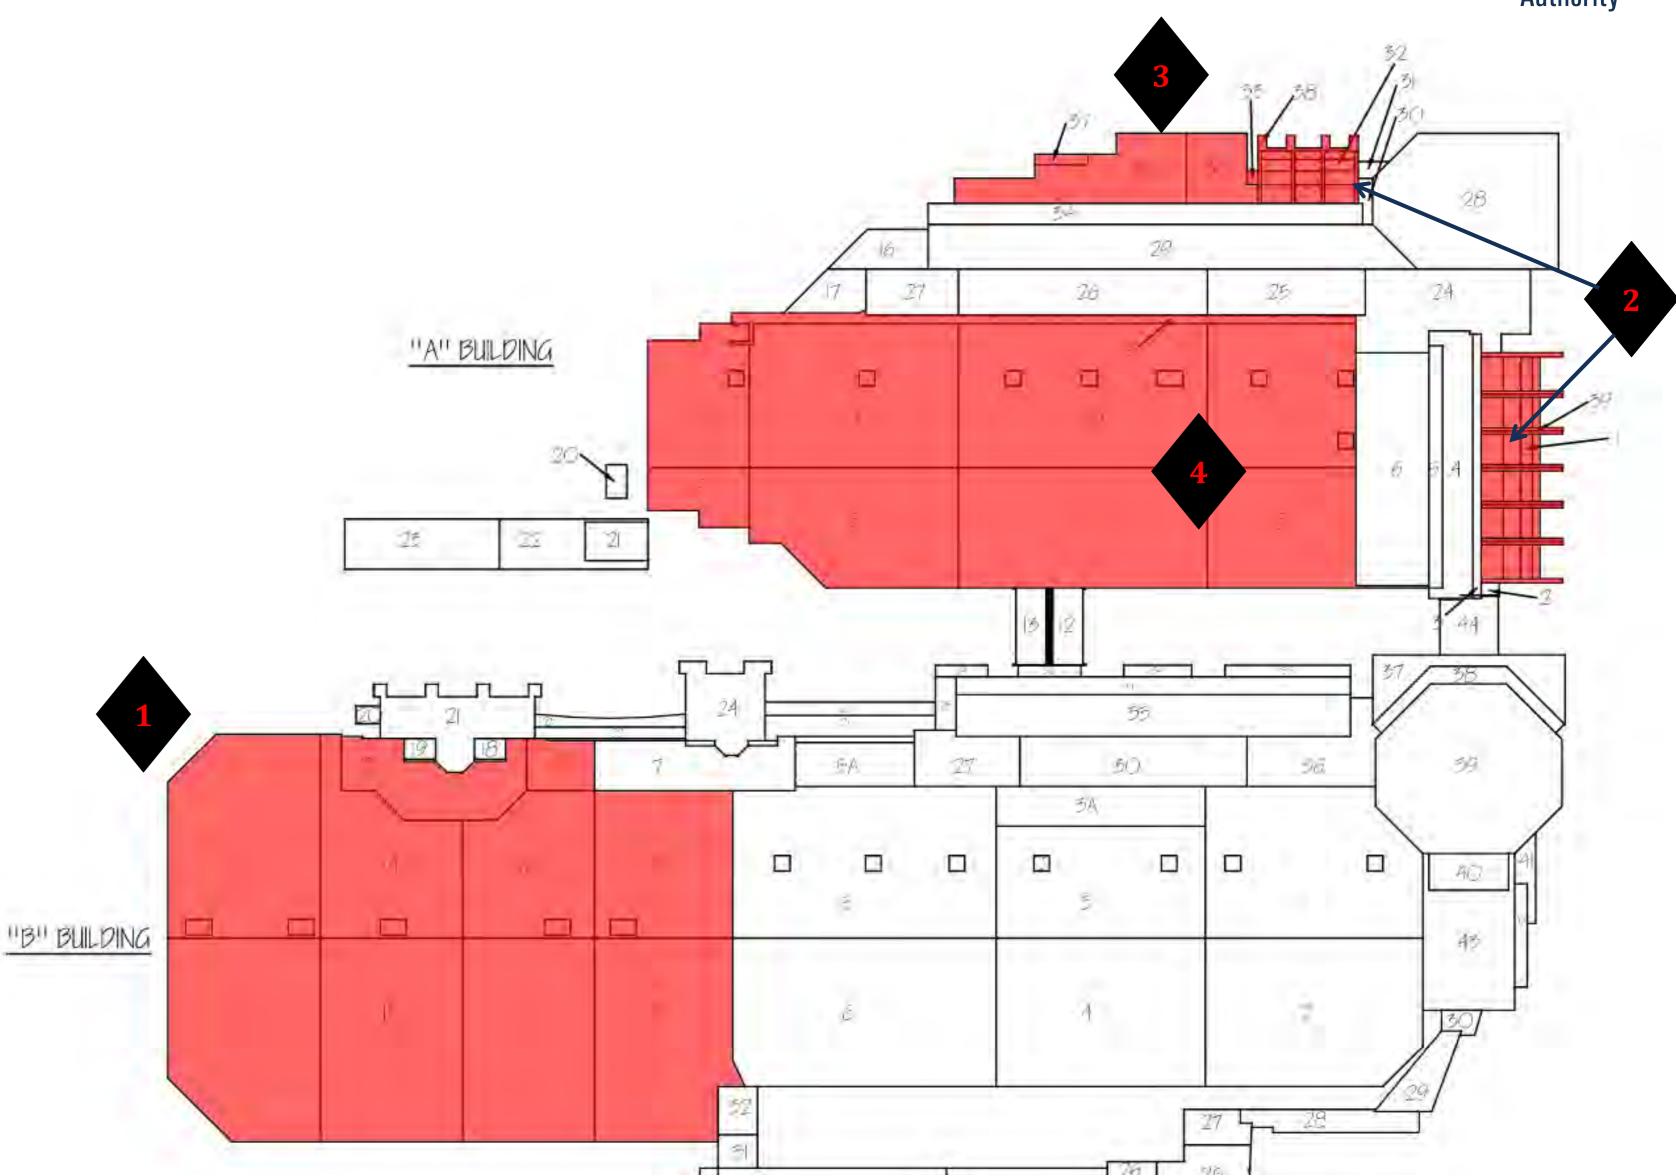

Re-Roofing Process – Priority 1 (Halls B4 – B5)



- Projected Start
 - Penthouse and RTU repairs July or August 2021
 - Re-Roofing Earliest start September 2021, more likely October/November

Re-Roofing Process – Priority 1 (Halls B4 – B5)



Process

- Partial tear-off
 - Remove roofing and protection board
 - Add insulation and new protection board
 - Add roofing membrane
- Two or three crews
- Will work on move-in/move-out days
- No work on event days
 - Rehearsals treated as event days
- No work when 20% rain chance or more
- Tear-off in early morning / new work during the day
- Limit day's work to area that can be completed and water-tight



Signia by Hilton

Project Information

- Project Manager: Otto Johnson & Ken Stockdell
- Project Scope: Construct a new 40 story, 975 room luxury hotel that would connect to Building C of the GWCC.
- Project Location: West Plaza & Former Georgia Dome Site

• Project Status

- Current Phase: Active Construction
- Construction Schedule: April 2021 December 2023


Misc. Hotel Project Items




- Gate 20 Drive Lane Work
 - Currently 1 lane access to Buildings B & C Loading Docks
 - Continuing Electrical Line Work
 - New Work on Sanitary Lines
 - Upcoming Work on Water Lines
 - Expecting all of this through July and August
- Temp Wall for "Knuckle" Area
 - Installation for Temporary Wall schedule for TBD
 - Continuing Exploratory Work and Drawings
 - Plastic Covering, Demo & Relocation, Wall Install, Glass Removal


Gate 20 Drive Lane & Temp Wall at Knuckle



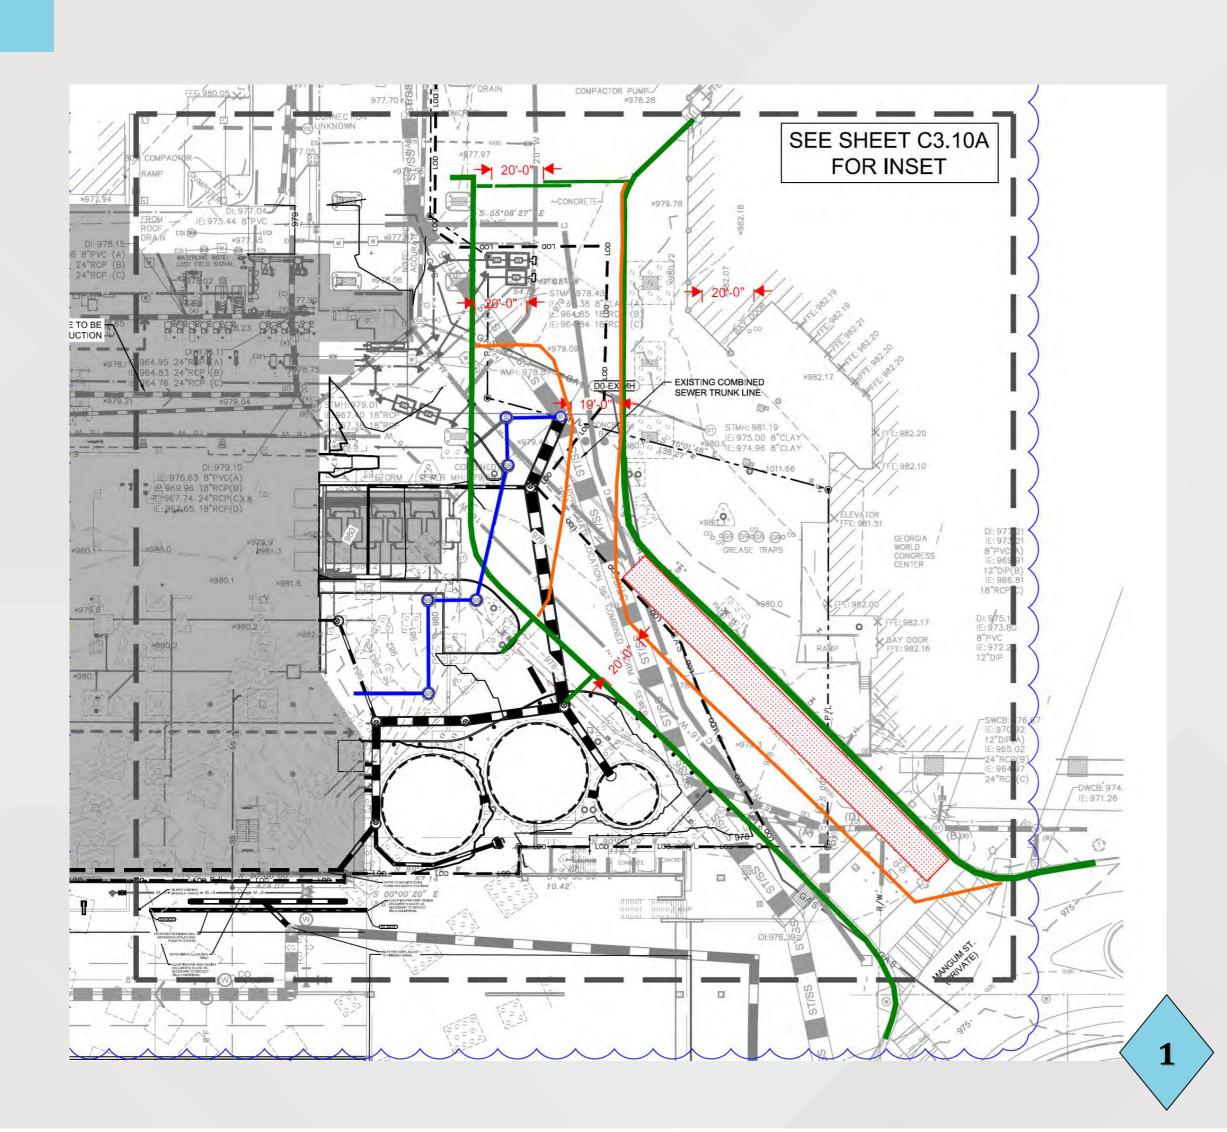

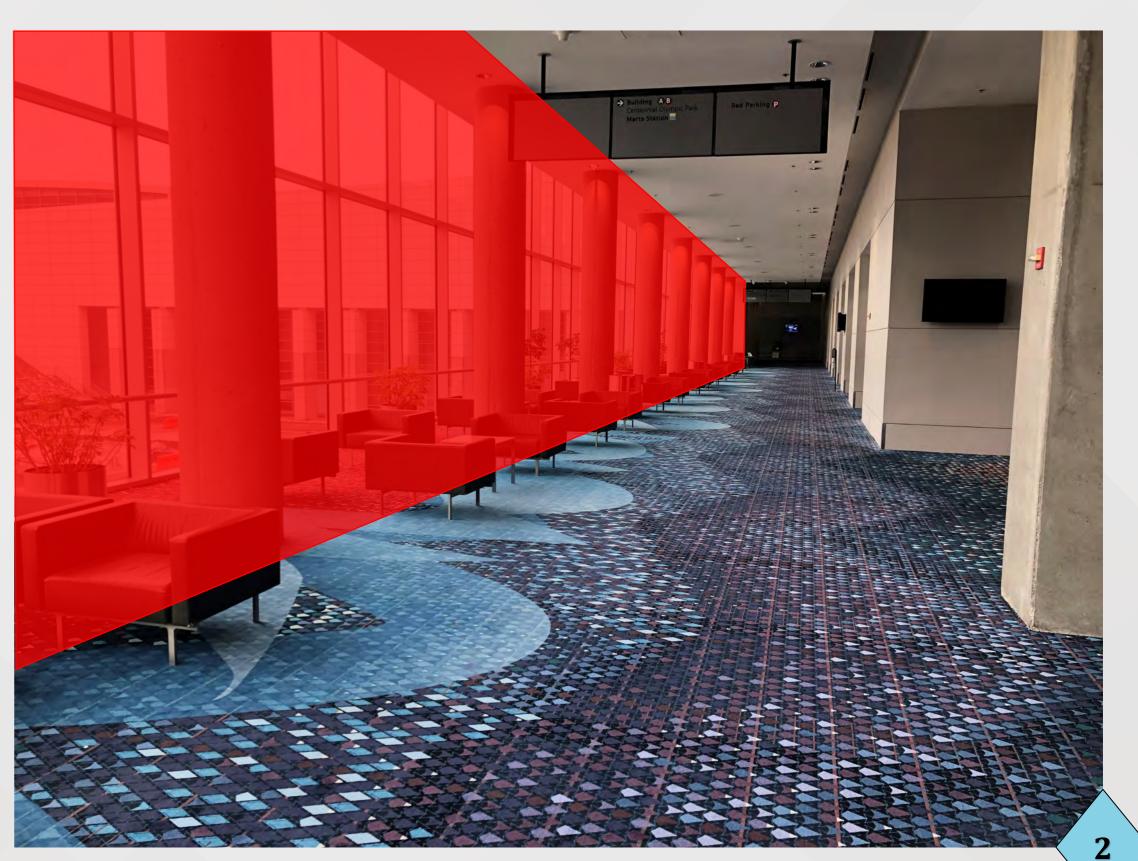





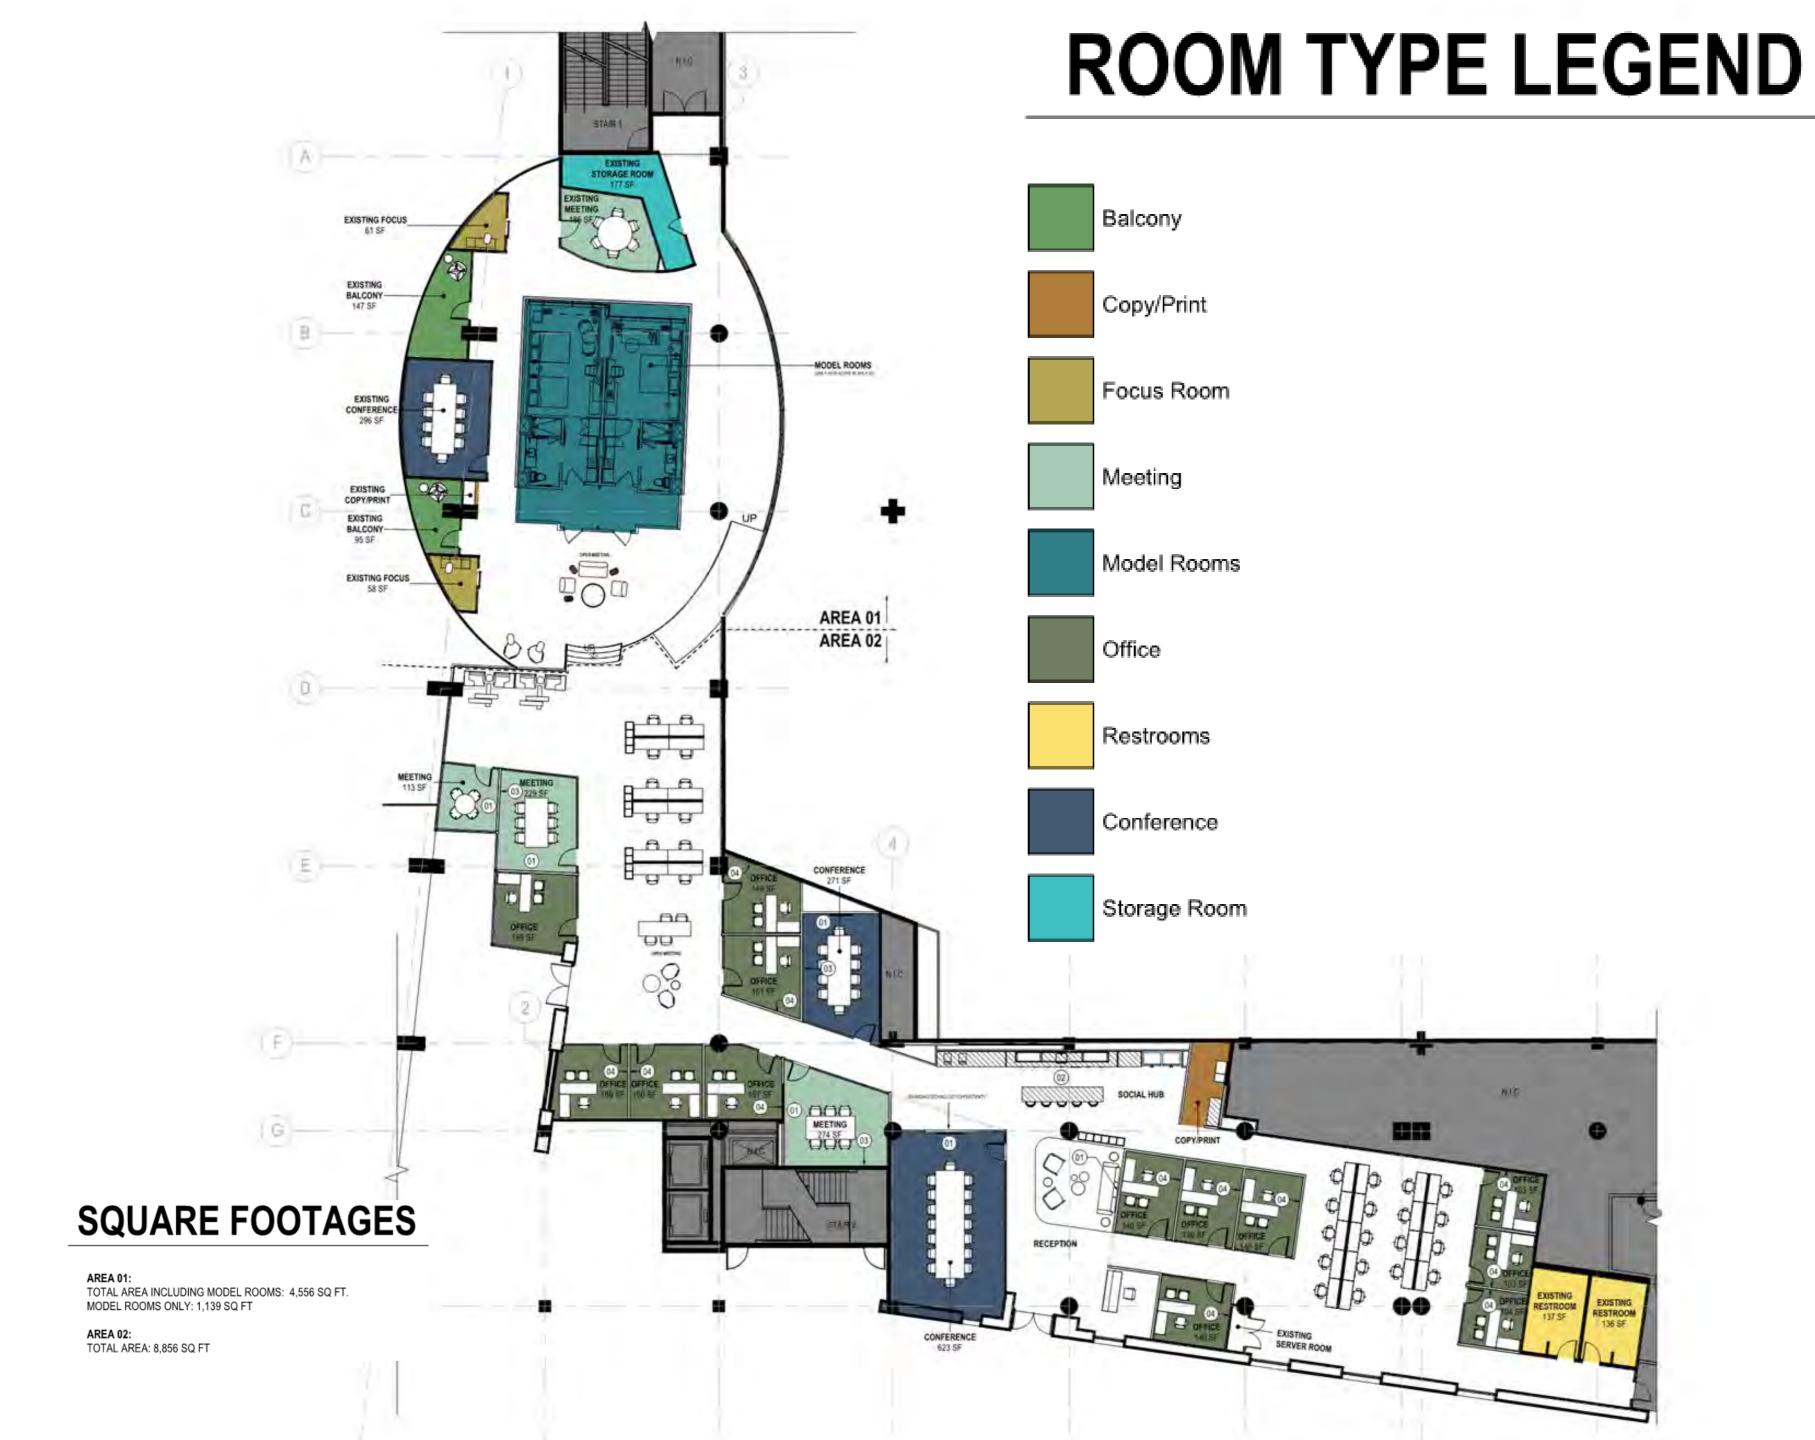


Sales Offices – Demo Work




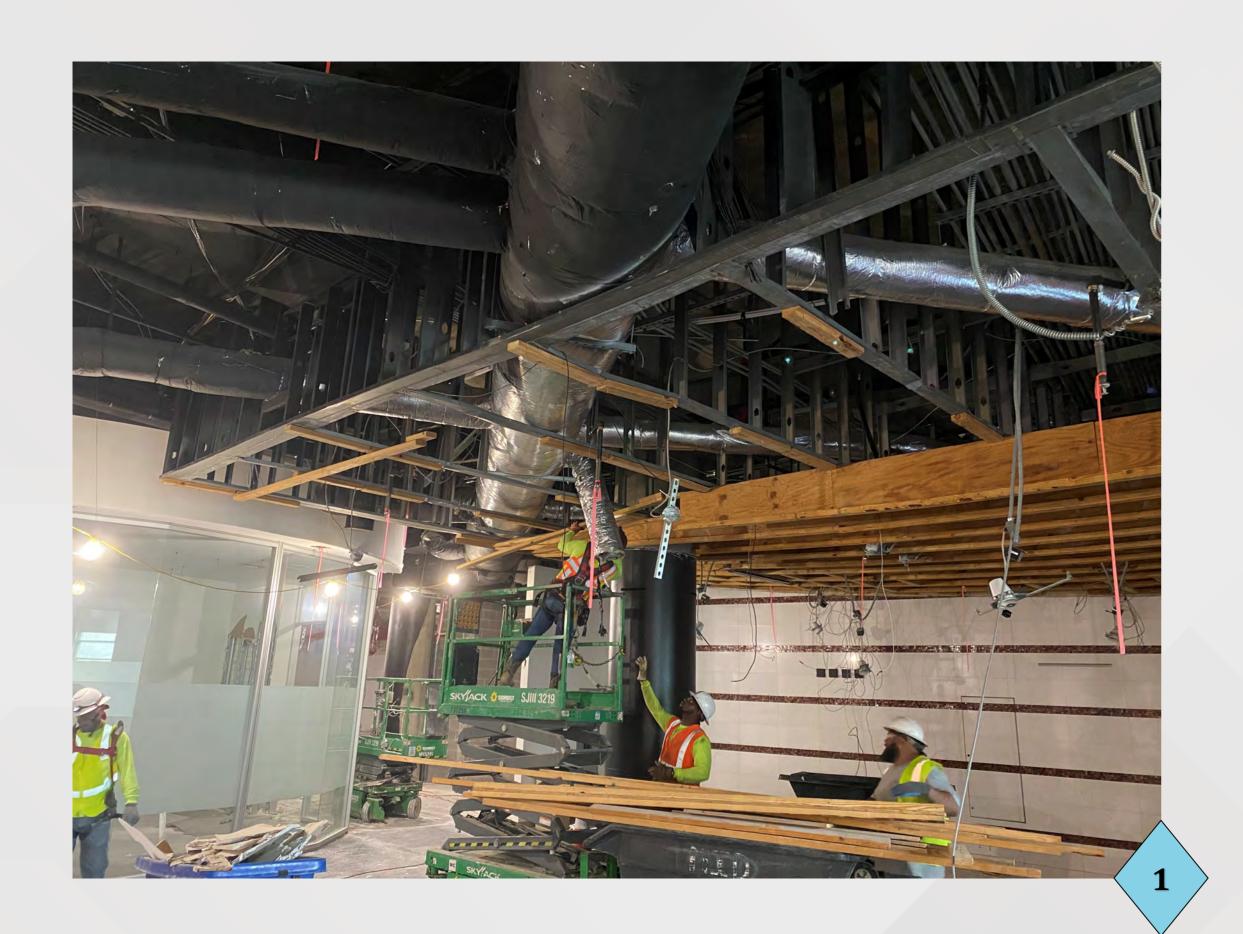

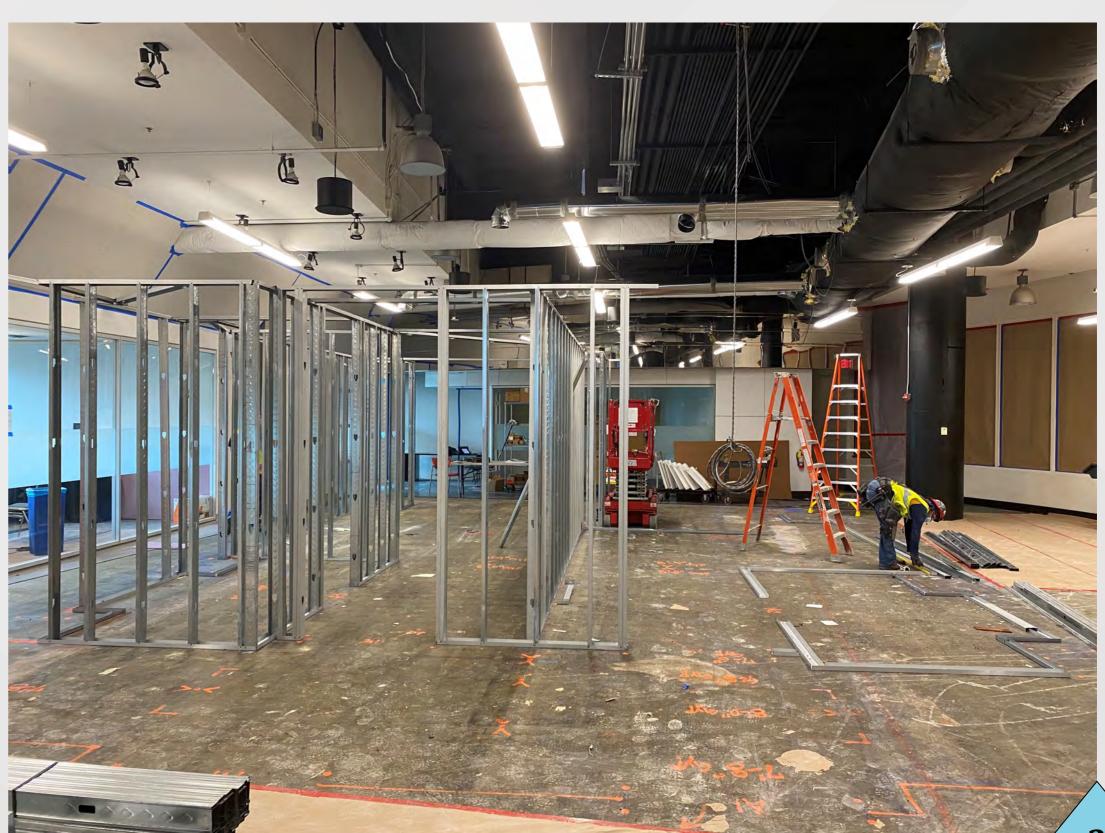

2

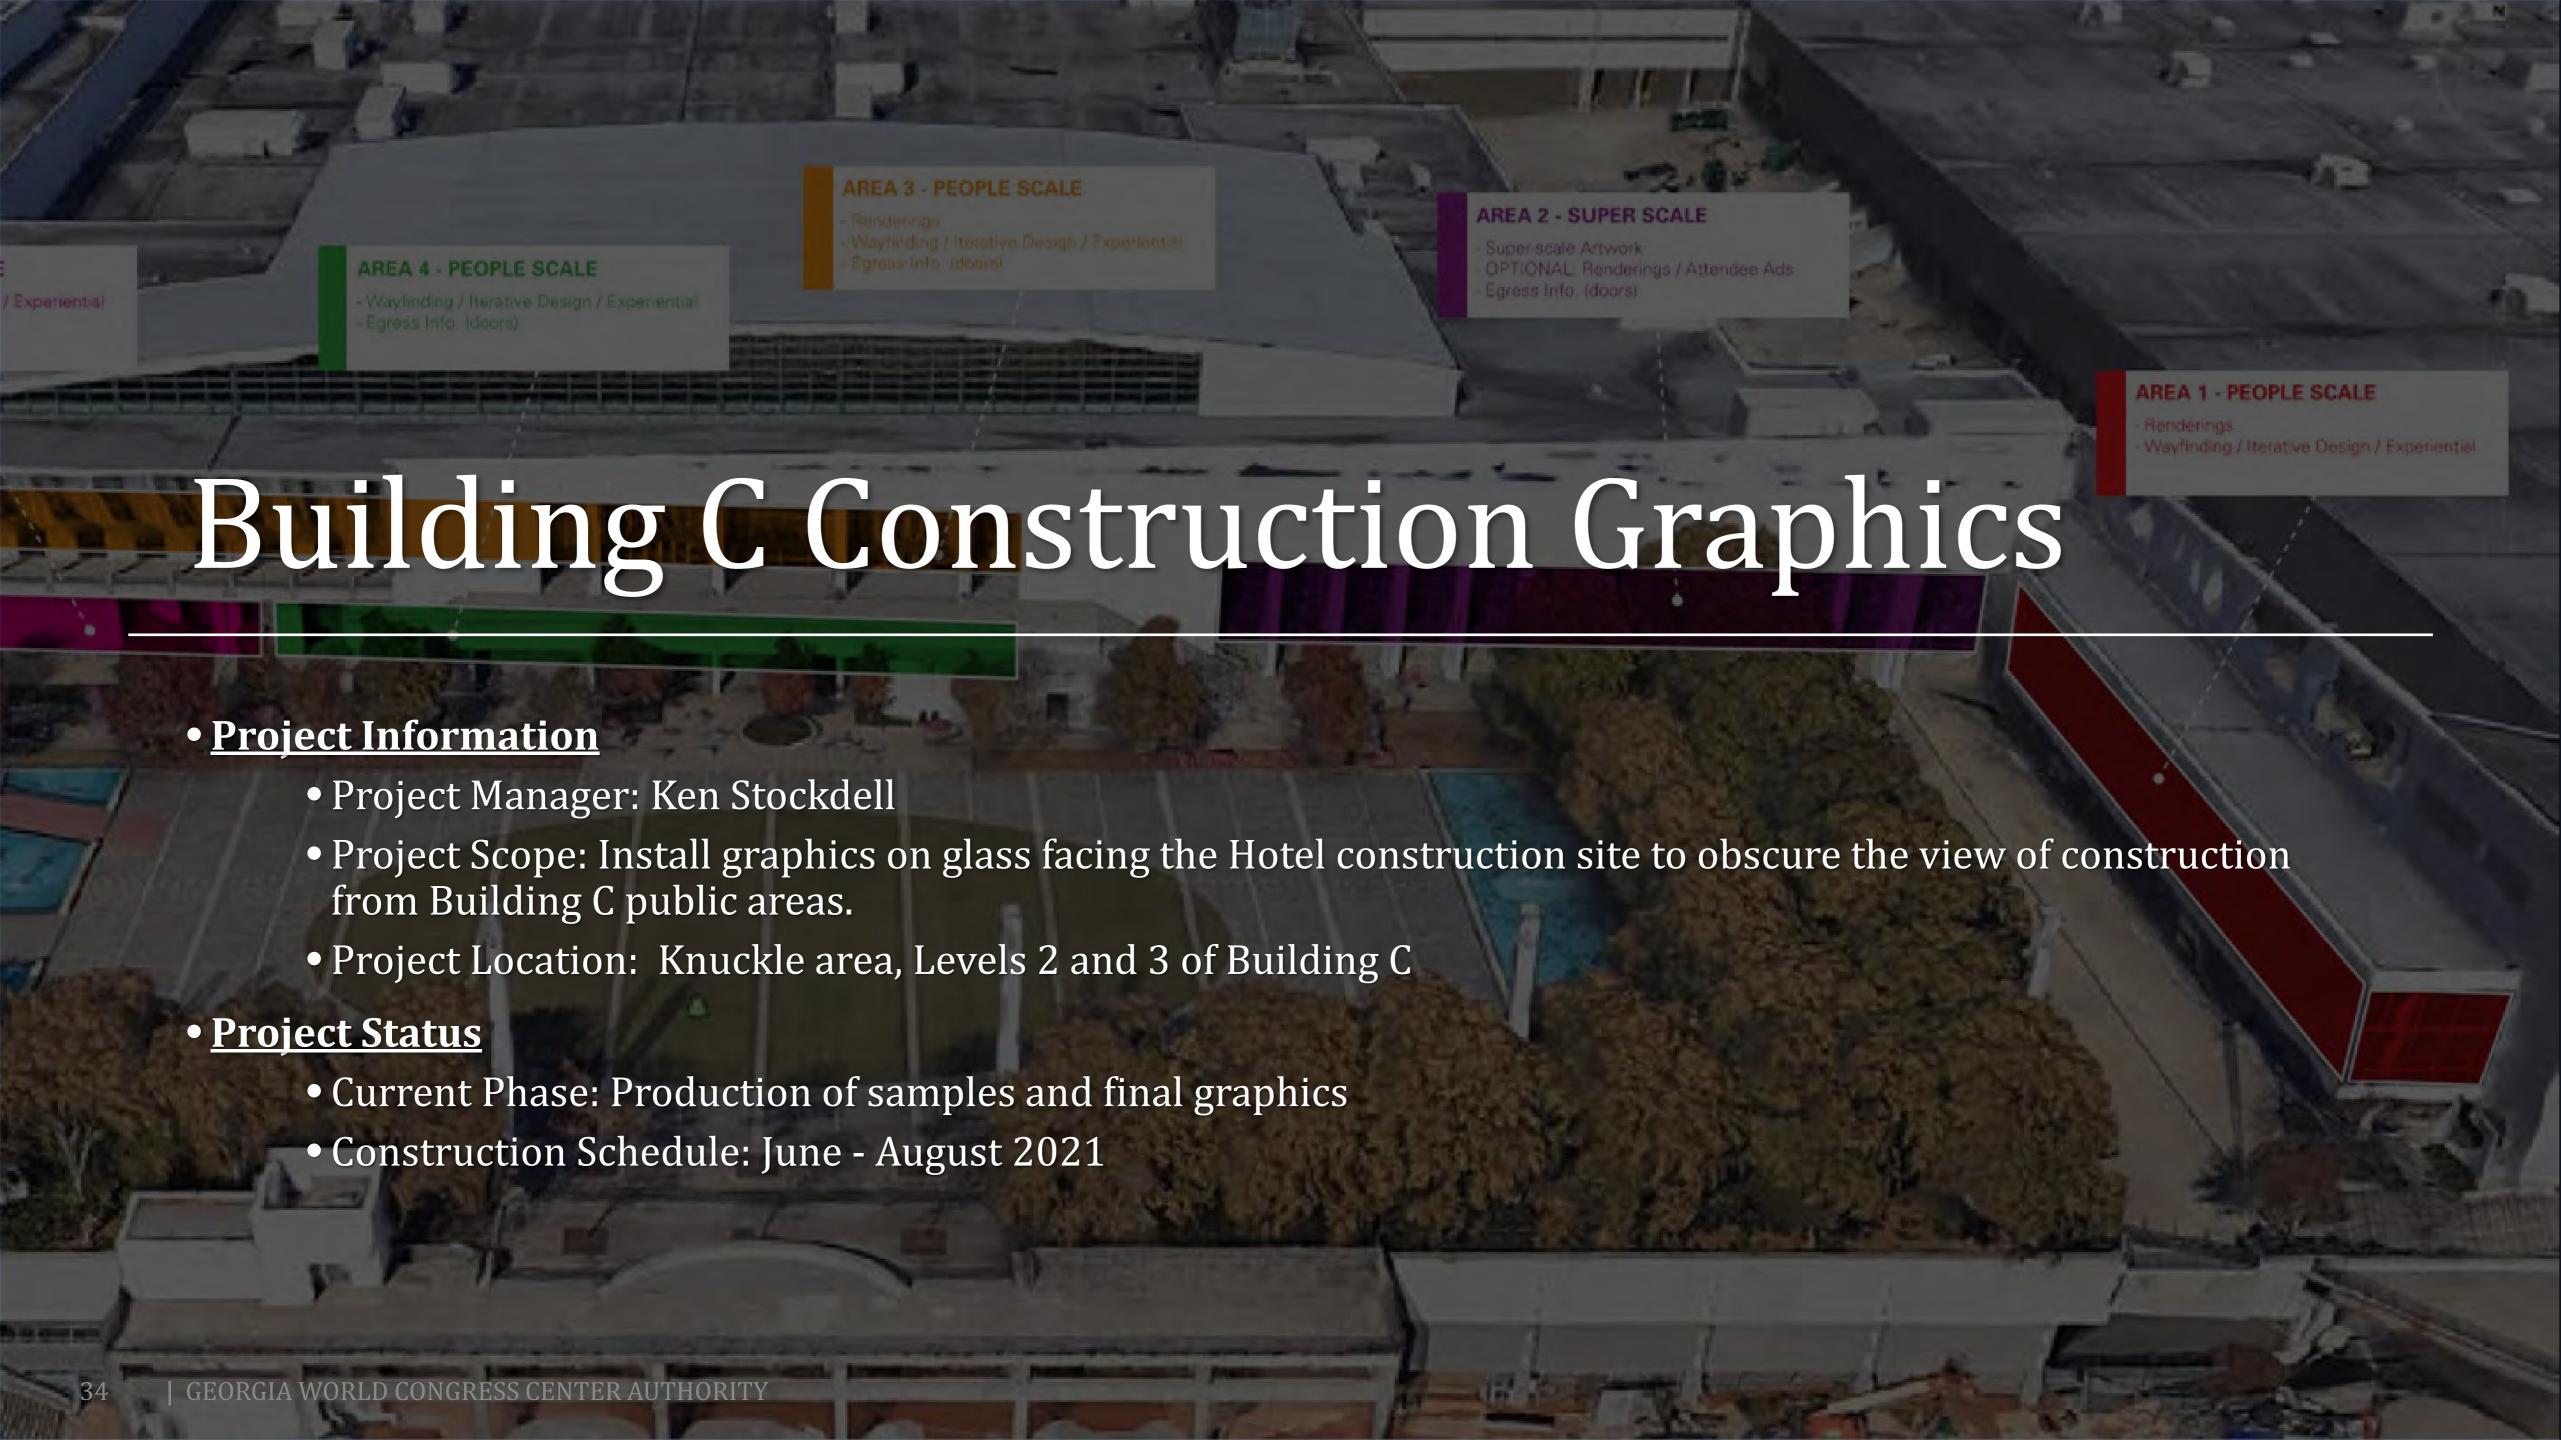

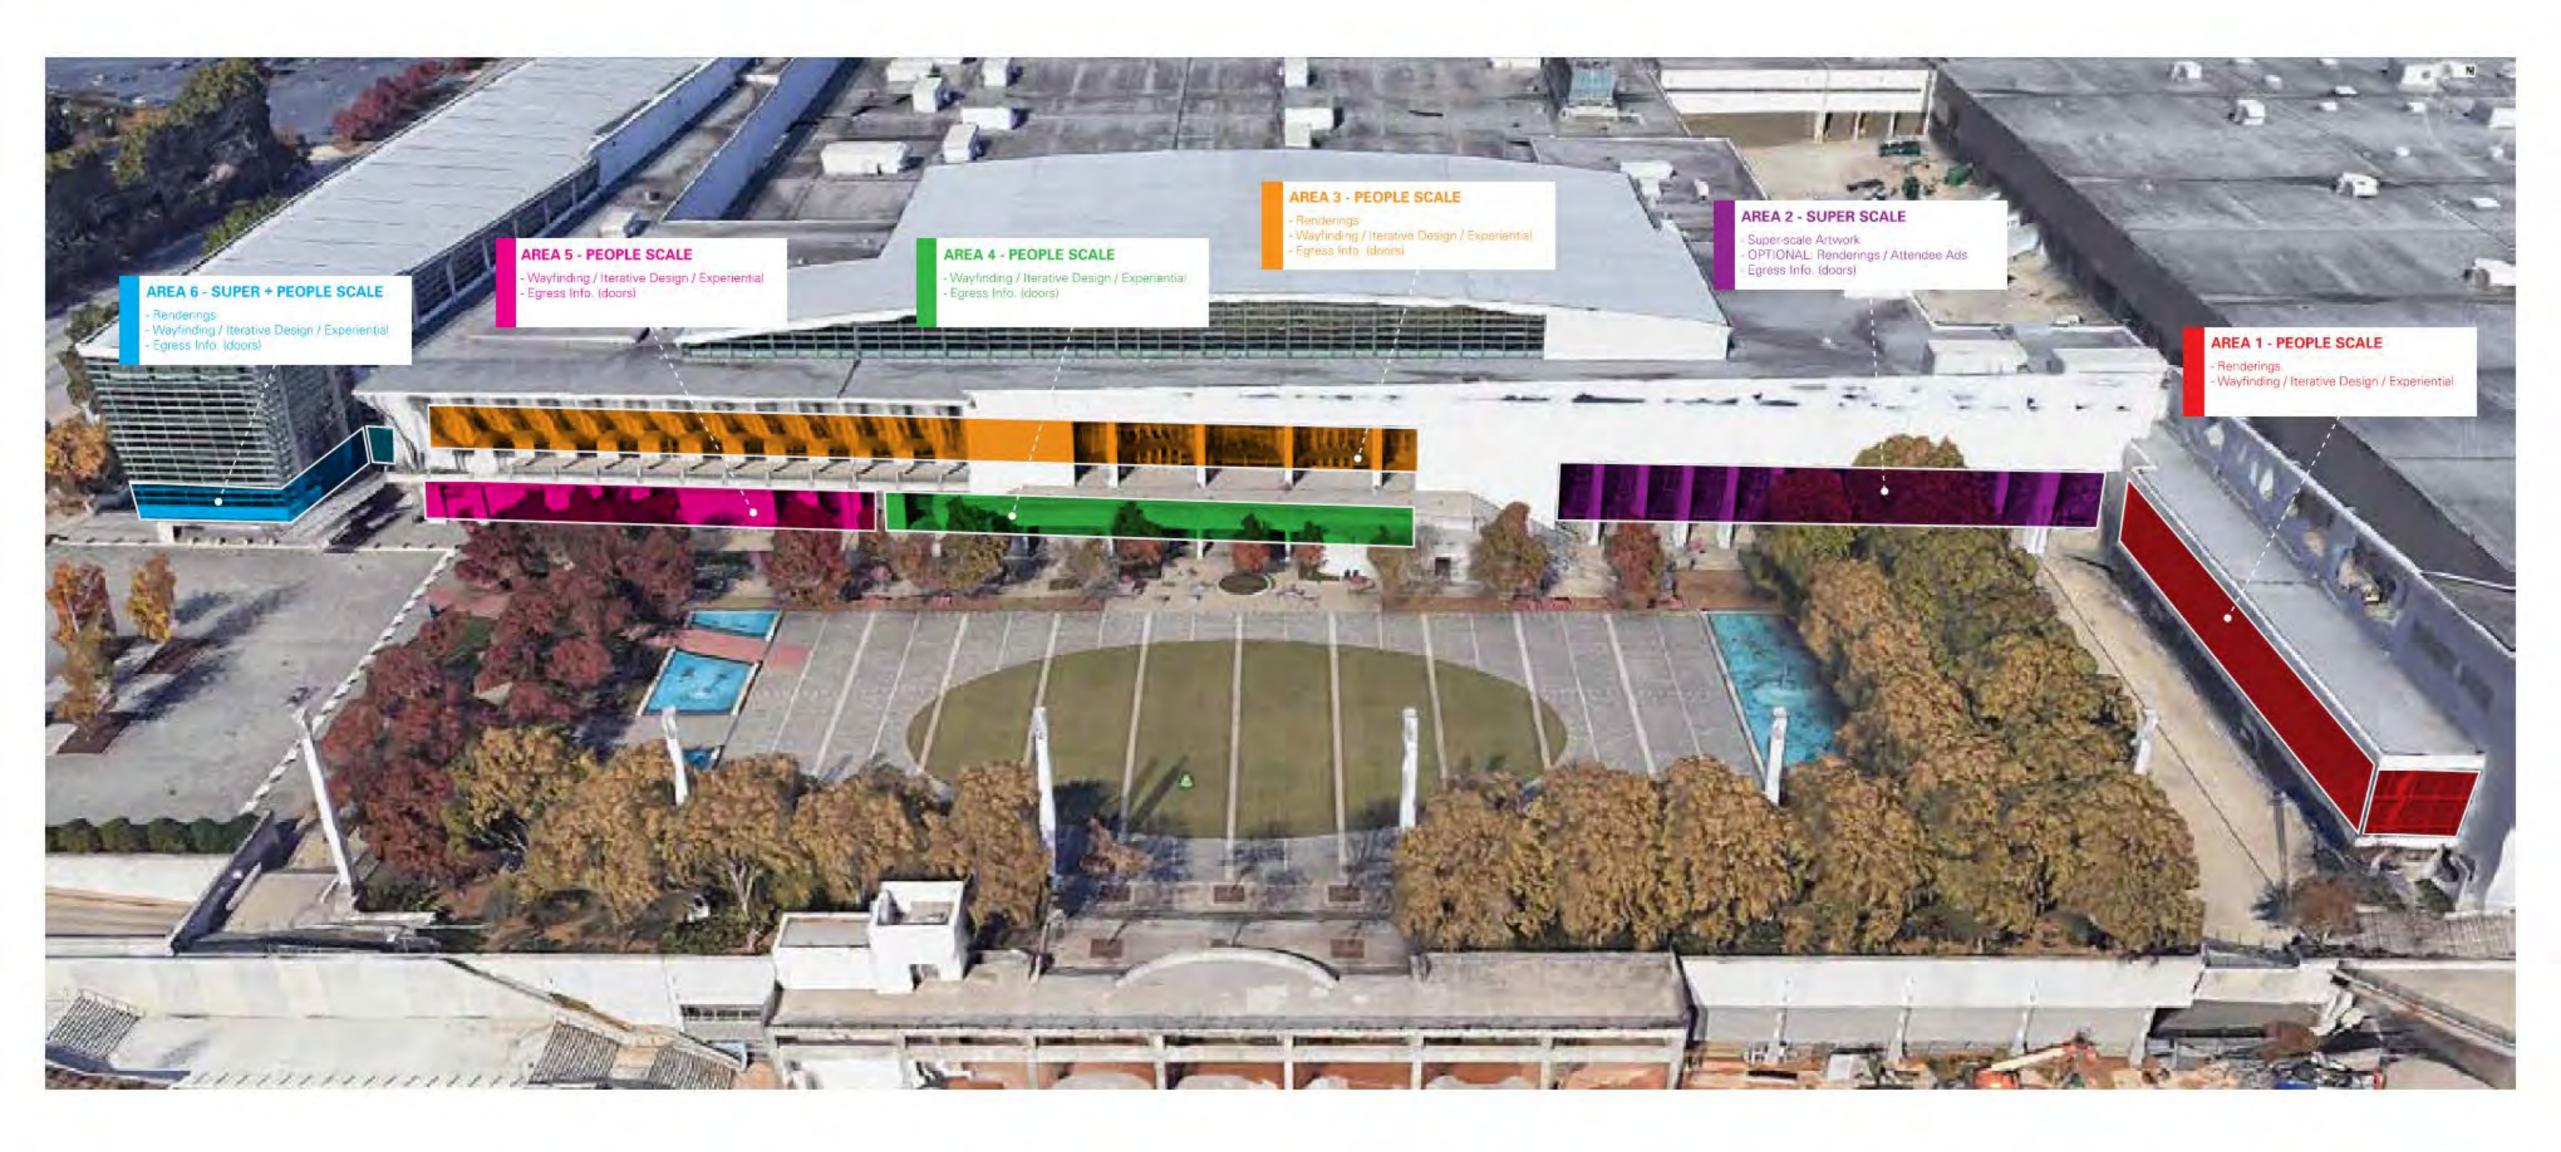

- 1 B/C Connector Corridor
- 2 Level 2 & 3, near C206

- Level 3, across from GA Ballroom
- 4 Level 2, along Gold Deck Entry
- Level 2, across from Special Event Space
- 6 Level 2 & 3, Turnaround Entry



Thank you for your continued support in the development of our campus!

Department of Project & Program Management July 8, 2021
