

# GWCCA Campus Development Project Updates

April 29, 2021

Department of Project & Program Management

# Today's Agenda



Campus Development Website  
AYIB Pedestrian Mall  
AYIB Transportation Depot  
GWCCA/Hilton Signia Hotel

# GWCCA Campus Development Website



## How to Access?

- 1. GWCCA Website
- 2. Under “Our Campus”
- 3. Select “Campus Development

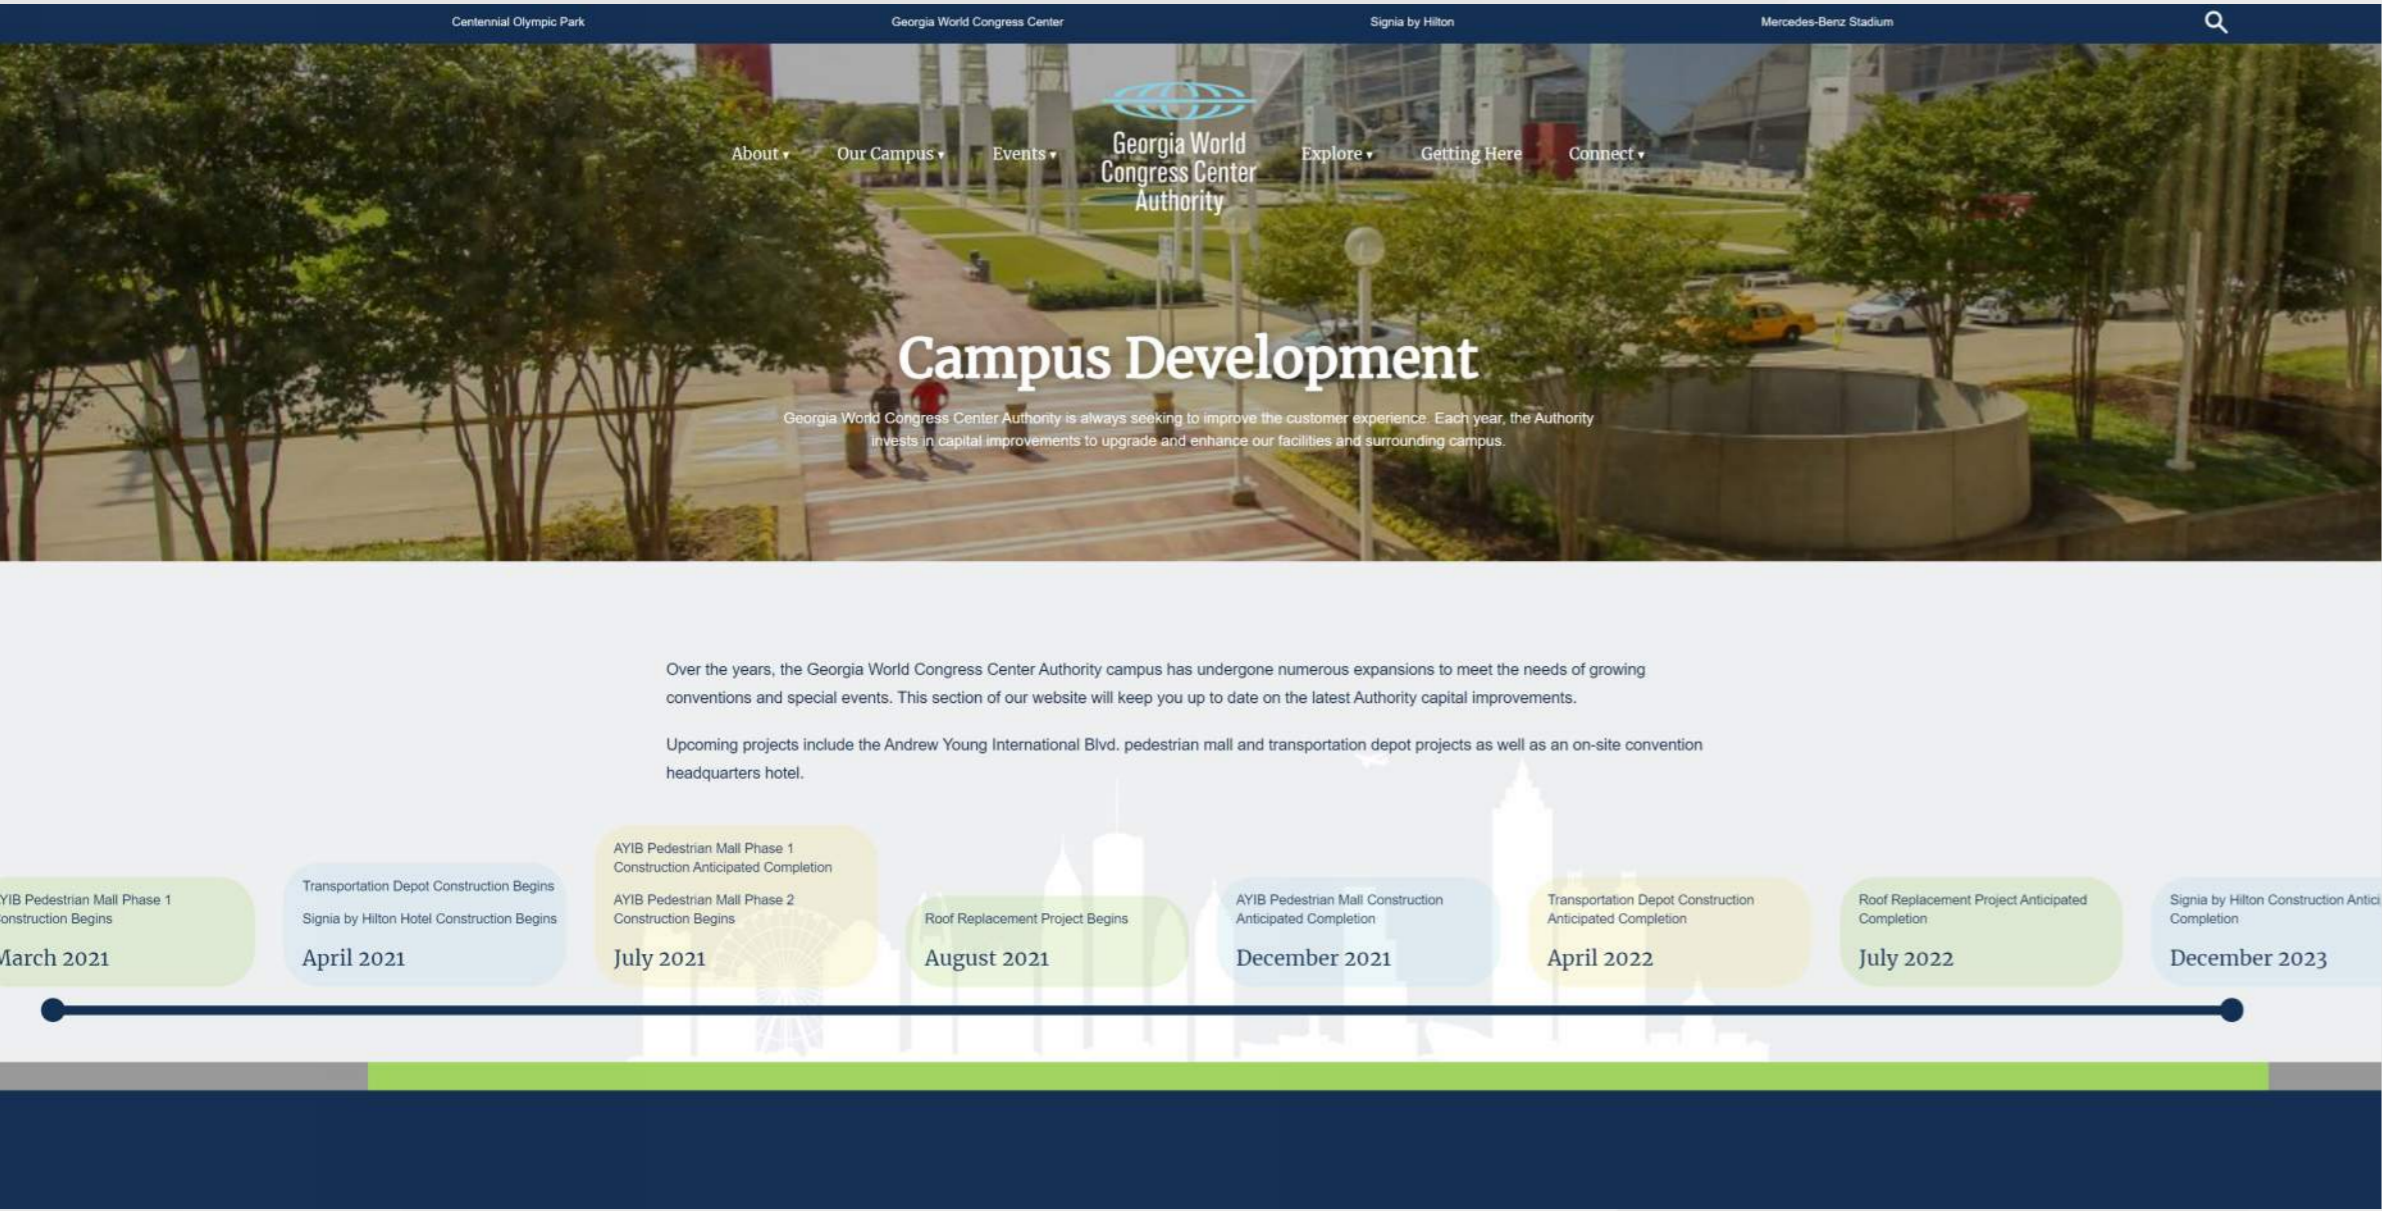

## What's Available?

- 1. Up to date information on schedule
- 2. Details on Key Projects
- 3. Current & Previous Master Decks

# Andrew Young International Blvd.

## • Pedestrian Mall

### • Project Information

- Project Manager: Ken Stockdell & Taylor White
- Project Scope: Extend COP pedestrian experience to GWCC building entrances and eventually leading to GWCCA Hotel. Create a safer pedestrian experience through the GWCCA Campus.
- Project Location: Current sidewalks & traffic lanes along Andrew Young International Blvd from Marietta St. to Centennial Olympic Park Drive. Improvements will also be made to the East Plaza.

### • Project Status

- Current Phase: Construction
- Construction Schedule: Mid-March – December 2021

## • Transportation Depot

### • Project Information

- Project Manager: Ken Stockdell & Taylor White
- Project Scope: Create a designated pick-up and drop-off area for all buses and taxi/rideshare vehicles. To improve traffic conditions by minimizing congestion and improving trip times. Create an alternative Red Deck entrance.
- Project location: Current green space between International Plaza and State Farm Drive and current Red Deck Entry & COP Drive.

### • Project Status

- Current Phase: Construction
- Construction Schedule: April 2021 – April 2022


# Andrew Young International Blvd Projects

Pedestrian Mall Site

Transportation  
Depot Site

# Andrew Young International Blvd Projects



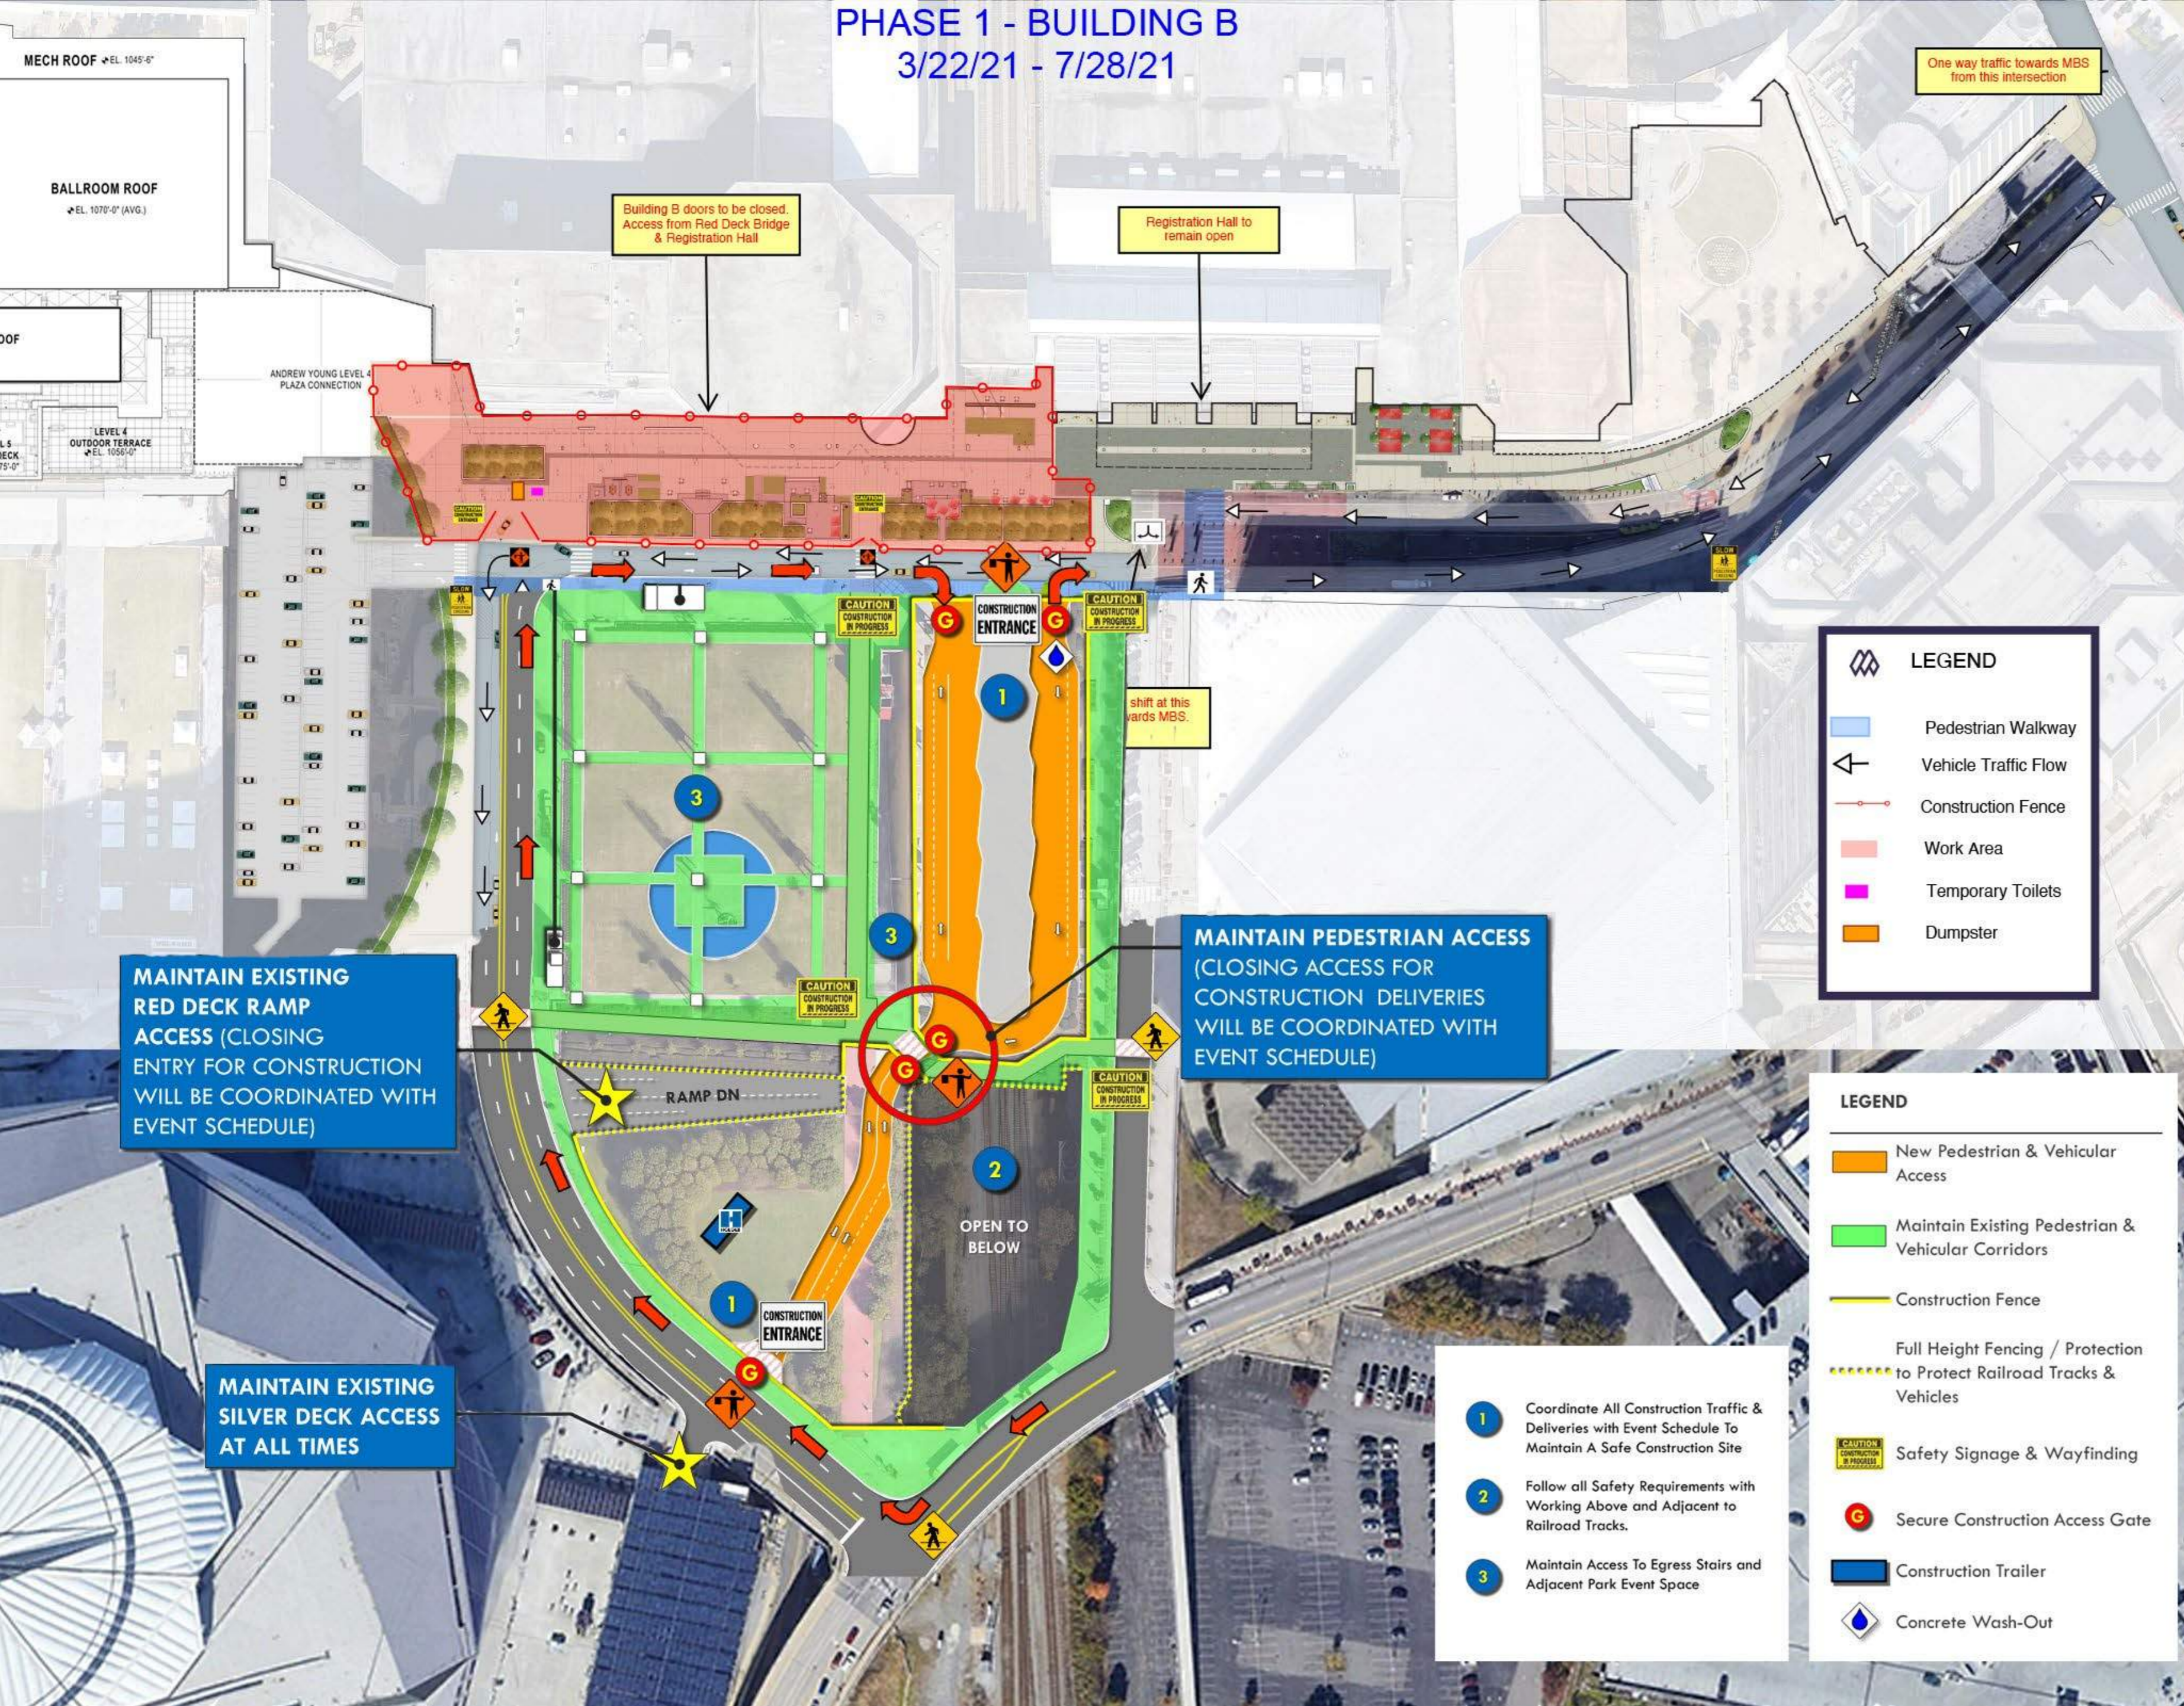

**Pedestrian Mall**  
**Phase 1**  
**3/22/21 - 7/28/21**

**Transportation Depot**  
**4/6/21 - 4/5/22**

# 4-Week Look-Ahead Schedule

Project	Activity	Start Date	Finish Date
Pedestrian Mall	Oculus Steel Infill	4/12/21	4/27/21
	Start overlay of concrete top coating	4/16/21	5/20/21
	CMU planters	4/19/21	5/12/21
	Pour Oculus Infill Concrete	4/28/21	5/4/21
	Footings for Light Poles	4/28/21	5/11/21
	Install Expansion Joints	4/30/21	5/20/21
	CMU for West Planter	5/2/21	5/7/21
	Stone at Planter Walls	5/3/21	5/28/21
	Electrical Cores for Canopy and Rough-in	5/6/21	5/26/21
	Plumbing Rough-in Hall A1	5/10/21	5/21/21
	Electrical Rough-in	5/10/21	5/21/21
	Frame Composite Decking	5/10/21	6/7/21
	Planter Curbs at Decks	5/13/21	5/21/21
	Waterproofing at Planters	5/13/21	6/3/21

# April 23 Drone Photo



# April 23 Drone Photo



# Construction Progress Photos



# 4-Week Look-Ahead Schedule

Project	Activity	Start Date	Finish Date
Transportation Depot	Strip Transportation Depot Area	4/12/21	5/21/21
	Strip South Drive Area	4/12/21	5/13/21
	Prepare/Excavate/Enabling Work for Micropiles	4/14/21	4/29/21
	Excavate East/West Pedestrian Pathway	4/28/21	4/30/21
	Foundation Micropiles	4/30/21	5/24/21
	Install Temporary East/West Pedestrian Pathway	5/3/21	5/7/21
	Remove Existing Slab Waterproofing at Concrete Ribs	5/6/21	6/17/21
	Structural Improvements	5/14/21	9/24/21

# April 23 Drone Photo



# April 23 Drone Photo





# GWCCA Hotel Project

---

- **Project Information**

- Project Manager: Otto Johnson, Ken Stockdell, and Taylor White
- Project Scope: Construct a new 40 story, 975 room luxury hotel that would connect to Building C of the GWCC.
- Project Location: West Plaza & Former Georgia Dome Site

- **Project Status**

- Current Phase: ACTIVE CONSTRUCTION!!!
- Construction Schedule: April 2021 – December 2023

# Current & Upcoming Activities

- Current Activities
  - Fence, Evac Tunnel & Fence Scrim Installation
  - Ensuring Lockdown of Site in Preparation for Events
  - Traffic Management, Contractor Access, and Gate 20
- Upcoming Activities
  - Decommissioning, Salvaging, and Removal 4/30
  - Hardscape Demo & Tree Removal in West Plaza
  - Lot 42 Demo for contractor takeover

# Exterior GWCCA Fencing – Fence Scrim



1



2



3



4

# Gate 20 Fence & Srim



Thank you for your continued support in  
the development of our campus!

Department of Project & Program Management  
April 29, 2021
